

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

November 14, 2019

Prepared For: Atlanta Public Schools

Prepared By: Tony Washington




Exterior Framing at New Addition



West Elevation Framing at New Addition



Ductwork Installation at New Addition

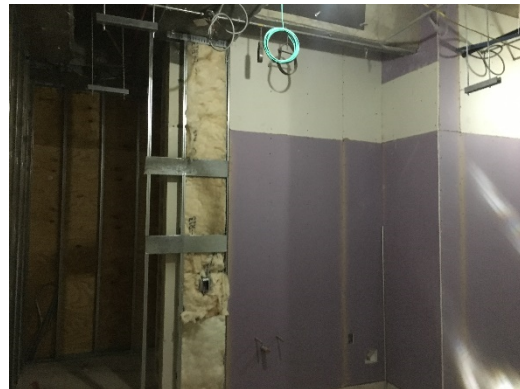

Interior Insulation Installation



East Elevation Final Grading



New Water Vault Installation

WEEKLY CONSTRUCTION PROGRESS REPORT

Humphries Elementary School

November 14, 2019



Last Week's Activities:

- Completed bent plate installation at building 2030
- Completed sprinkler system installation at building 2033 & 2040
- Completed domestic water reroute
- Poured building 2030 elevated slab
- Complete underground kitchen plumbing
- Began door frame installation at building 2032
- Began roof installation at building 2033 & 2040
- Continued drywall installation at building 2031

This Week's Activities:

- Completed bent plate installation at building 2030
- Completed domestic water reroute
- Continued roof installation at building 2033 & 2040
- Continued drywall installation at building 2031
- Began rood decking on new addition
- Began exterior framing at new addition
- Began interior framing at new addition
- Completed courtyard storm line installation
- Began final grade at East elevation
- Began duct work installation at new addition
- Continued level 2 sprinkler installation

Next Week's Activities:

- Begin Stormtech at parking lot
- Continue exterior framing at new addition
- Continue interior framing at new addition
- Complete roof installation at building 2033 & 2040
- complete roof decking at building 2030
- Begin MEP installation at new addition
- Begin canopy foundations
- Pour metal stair stringers
- Continue level 2 sprinkler system

Schedule:

- Status: On Schedule
- Date of substantial Completion: June 2020

Budget:

- Construction Budget: \$9,650,000
- Budget Status: On Budget
- Gross Billed to Date: \$1,957,883
