



Weekly Construction Progress Report

**Addition and Renovation work to
Morningside Elementary School
Week Ending: 06/25/2021**

PARRISH
CONSTRUCTION GROUP

Weekly Updates

Upcoming Activities

- Week of June 28th
 - Sitework continues
 - Interior demolition continues
 - Selective plumbing fixture demolition
 - Concrete cutting for underground plumbing
 - Underground plumbing rough-in begins
 - Site demolition begins
 - Includes excavators and other heavy equipment
- Week of July 5th
 - Sitework continues
 - Mechanical demolition begins
 - Electrical demolition begins
 - Plumbing underground rough-in continues
- Week of July 12th
 - Sitework continues
 - Mechanical demolition continues
 - Electrical demolition continues
 - Plumbing underground rough-in continues



Budget

BUDGET

Construction Budget

- \$17,100,000

Budget Status

- \$894,522.11



ADDITIONAL INFO

- Completed By
 - Ben Fairchild
- Copies To
 - Danny Gutlay, APS
 - Sandra Horton, APS
 - Jim Fallon, PCG
 - A.J. Segel, PCG
 - Chris Hubbard, PCG



Photo/Activity Updates

Erosion control measures




Storm drainage installation



Photo Updates

Concrete cutting for underground plumbing rough-in

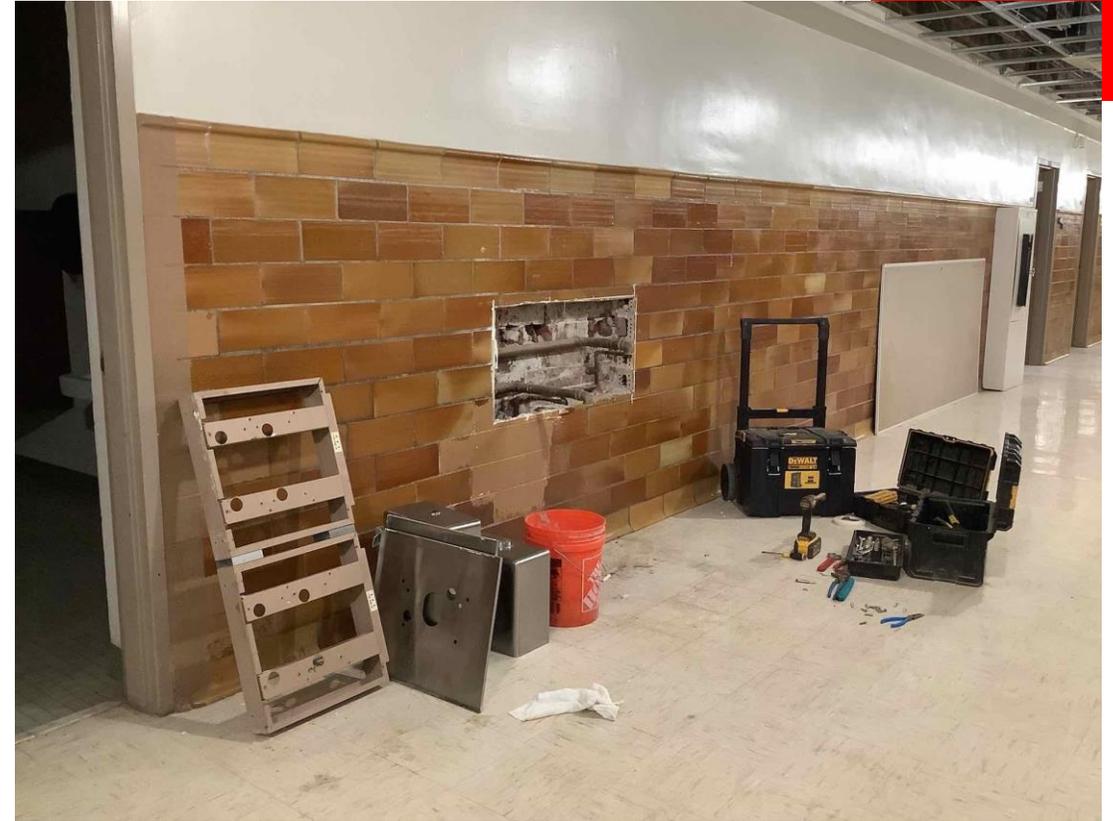

Selective plumbing fixture demolition

