



# Weekly Construction Progress Report

## Morningside Elementary School

Week Ending: 08/20/2021

### THIS WEEK

- Sitework continues
  - Storm drainage piping installation
  - Building pad grading
- Interior wall framing begins in Art/STEM rooms
- Interior wall framing continues in area B
- Mechanical equipment relocation continues
- Electrical rough-in continues throughout building
- Ductwork installation at media center and kitchen
- Plumbing rough-in continues throughout building
- New kitchen layout Ductwork installation
- Gas piping rough-in continues
- Interior demolition continues
- Drywall delivery
- Spiral duct delivery
- Site demolition for cafeteria addition begins

### NEXT WEEK: 08/23/21 – 08/27/21

- Sitework continues
  - Storm drainage piping installation
  - Building pad grading
  - Underground storm pond installation
- Electrical demolition continues throughout building
- Mechanical equipment relocation continues
- Electrical rough-in continues throughout building
- Plumbing rough-in continues throughout building
- Steel channel installation at parking deck
- Ductwork installation continues
- Gas piping rough-in continues
- Interior demolition continues
- Parking garage steel begins
- Sheetrock begins in area A

### BUDGET

#### Construction Budget

\$17,600,000.00

#### Budget Status


\$1,290,650.35

Completed By:  
Ben Fairchild

**PARRISH**  
CONSTRUCTION GROUP

# Photo/Activity Updates

Interior framing at art/STEM room

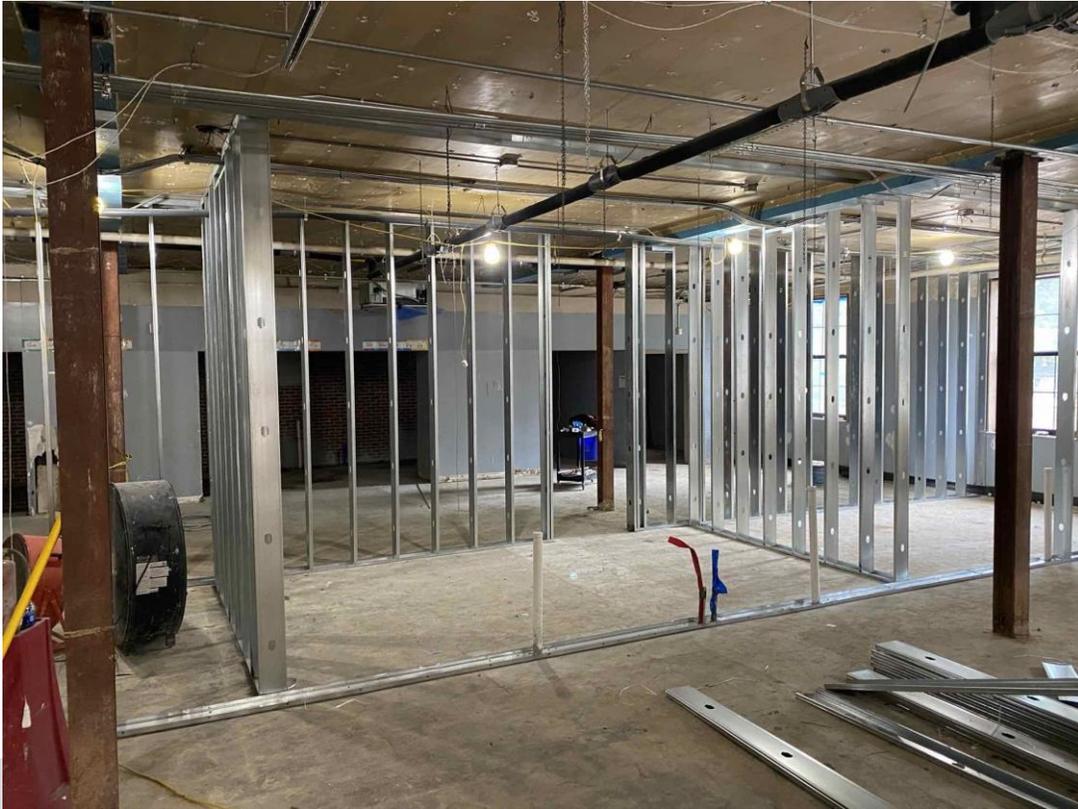


Drywall material delivery



# Photo/Activity Updates

Water heater relocation

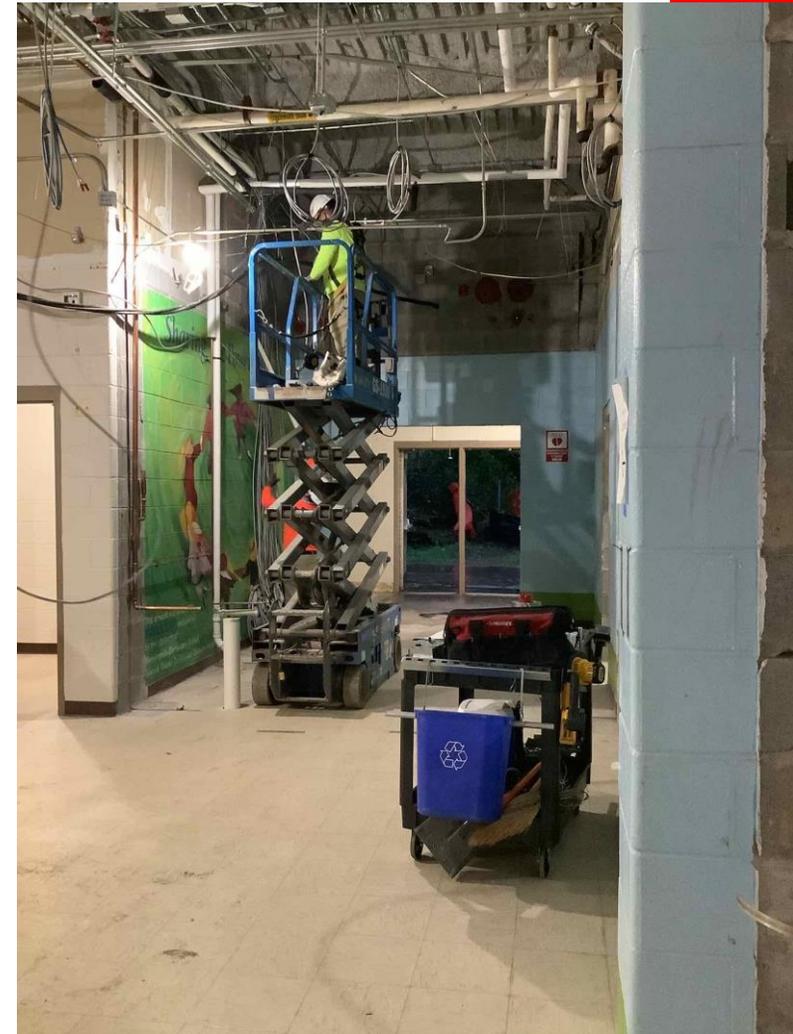

Plumbing overhead installation



# Photo/Activity Updates

Existing storm drainage demolition



Duct installation in new kitchen

