



Weekly Construction Progress Report

Morningside Elementary School

Week Ending: 10/15/2021

THIS WEEK

- Sitework continues
 - Grease trap installation finishes
- Mechanical equipment relocation continues
- Mechanical, electrical and plumbing rough-in continues throughout building
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Door frame installation continues
- Plaster repair continues at Area A and B
- Batt insulation installation continues
- Interior painting begins at Area A
- Selective demolition for cafeteria structural steel
- Rebar for new gym footings
- Cafeteria addition structural steel installation
- Concrete for new gym footings

NEXT WEEK: 10.18.21 – 10.22.21

- Sitework continues
 - Site grading
- Mechanical equipment relocation continues
- Mechanical, electrical and plumbing rough-in continues throughout building
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Door frame installation continues
- Plaster repair continues at Area A and B
- Batt insulation installation continues
- Interior painting continues at Area A
- Hard ceiling installation in restrooms
- Fire extinguisher cabinet block-outs
- Concrete for new gym footings

BUDGET/SCHEDULE

Construction Budget

\$17,600,000.00

Budget Status

\$2,395,124.47

Substantial Completion:

July 25, 2022

Schedule Status:

On Schedule

Completed By:

Ben Fairchild

PARRISH
CONSTRUCTION GROUP

Photo/Activity Updates



Photo/Activity Updates

Grease trap installation



Rebar for new gym footings and elevator shaft



Photo/Activity Updates

Cafeteria addition structural steel




Site grading following retaining wall demolition



Photo/Activity Updates

Mechanical, Electrical and Plumbing rough-in at kitchen

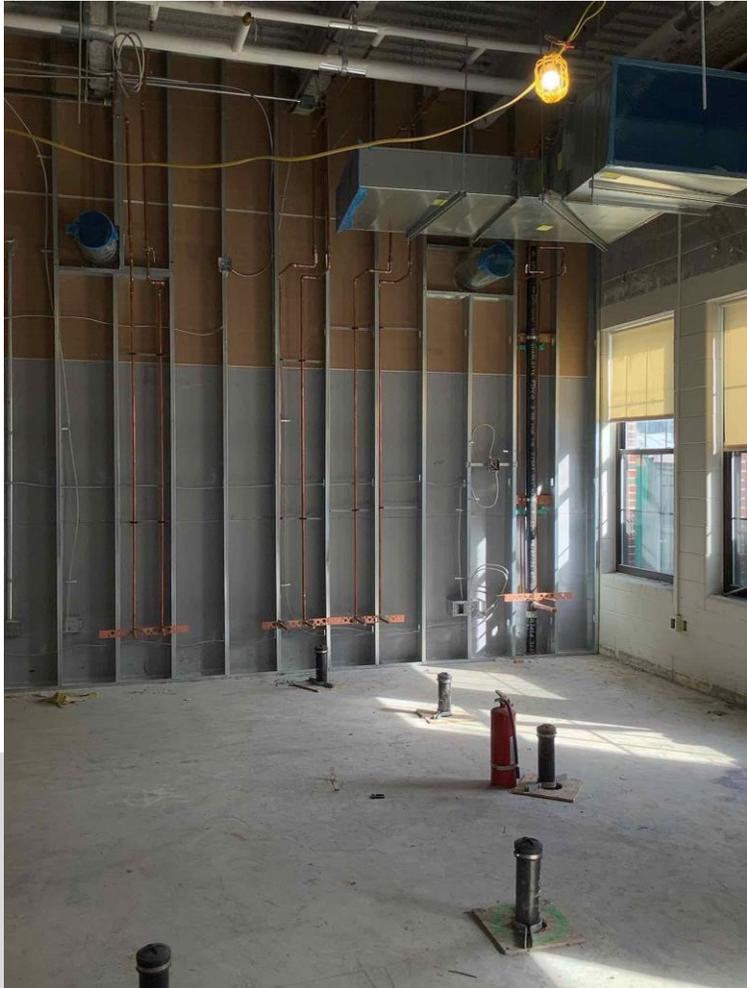

Water heater installation

