



Weekly Construction Progress Report

Morningside Elementary School

Week Ending: 12/24/2021

THIS WEEK

- Mechanical and electrical rough-in continues throughout building
- Low voltage rough-in continuing
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation continues
- Hard ceiling installation continues
- Interior painting continues in Area A and Area B
- Cafeteria courtyard yard drains installed
- Retaining wall install at cafeteria finishes
- Steel erection continuing at new addition
- Replacement of standing seam metal roof beginning

NEXT WEEK: 12.27.21 – 12.31.21

- Mechanical and electrical continues throughout building
- Low voltage rough-in continues
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation continues
- Hard ceiling installation continues
- Interior painting continues in Area A
- Steel erection continuing at new addition
- Second floor decking installation
- Replacement of standing seam metal roof beginning
- New Years break 12-31 to 01-01

BUDGET/SCHEDULE

Construction Budget

\$17,600,000.00

Budget Status

\$7,885,894.73

Substantial Completion:

July 25, 2022

Schedule Status:

On Schedule

Completed By:

Chris Hubbard

PARRISH
CONSTRUCTION GROUP

Photo/Activity Updates

New addition structural steel



New addition structural steel



Photo/Activity Updates

Cafeteria retaining wall



Cafeteria area



Photo/Activity Updates

Ceiling grid installed in hallway




Low voltage wire installation



Photo/Activity Updates

Classroom painting

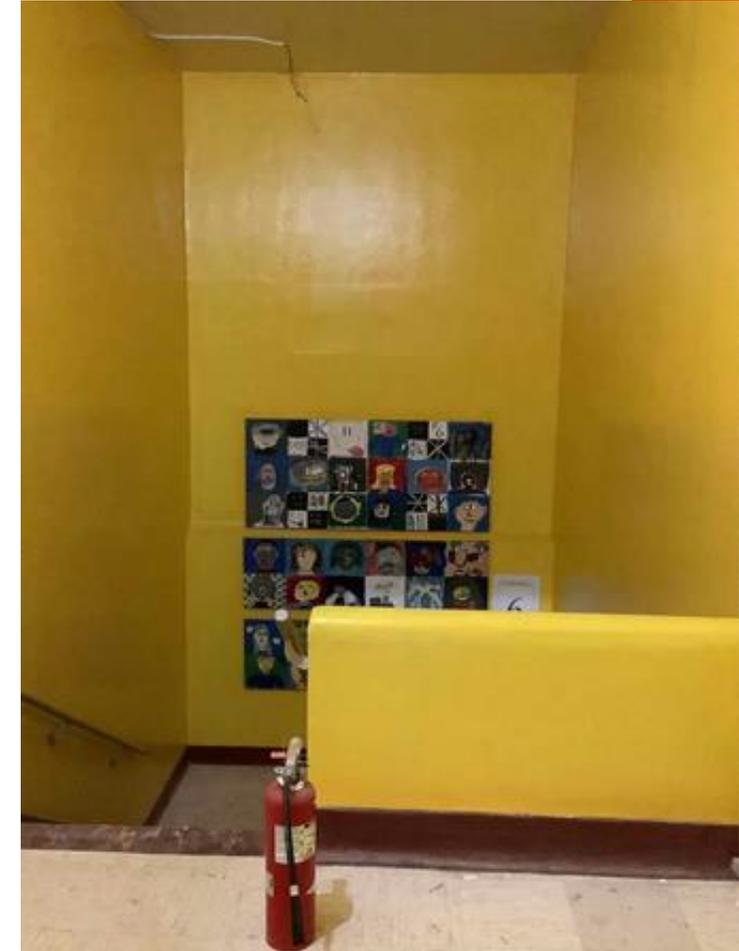

Stairway paint

