



# Weekly Construction Progress Report

## Morningside Elementary School

Week Ending: 01/21/2022

### THIS WEEK

- Mechanical and electrical rough-in continues throughout building
- Low voltage rough-in continuing
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation continues
- Hard ceiling installation continues
- Interior painting continues in Area A and Area B
- Steel erection continuing at new addition
- Replacement of standing seam metal roof continuing
- Curtainwall clips being installed
- Second floor concrete slab placement
- Parapet framing beginning
- Roof decking install beginning

### NEXT WEEK: 01.24.22 – 01.28.22

- Mechanical and electrical continues throughout building
- Low voltage rough-in continues
- Sheetrock continues throughout building
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation continues
- Hard ceiling installation continues
- Interior painting continues in Area A and Area B
- Steel erection continuing at new addition
- Replacement of standing seam metal roof continuing
- Curtainwall clips install continuing
- Parapet framing continuing
- Roof deck install continuing

### BUDGET/SCHEDULE

#### Construction Budget

\$17,600,000.00

#### Budget Status

\$8,839,447.43

#### Substantial Completion:

July 25, 2022

#### Schedule Status:

On Schedule

Completed By:

Chris Hubbard

**PARRISH**  
CONSTRUCTION GROUP

# Photo/Activity Updates

New addition structural steel



Parapet framing beginning



# Photo/Activity Updates

Second floor concrete pour complete




Roof curbs delivered



# Photo/Activity Updates

Cafeteria brick completion

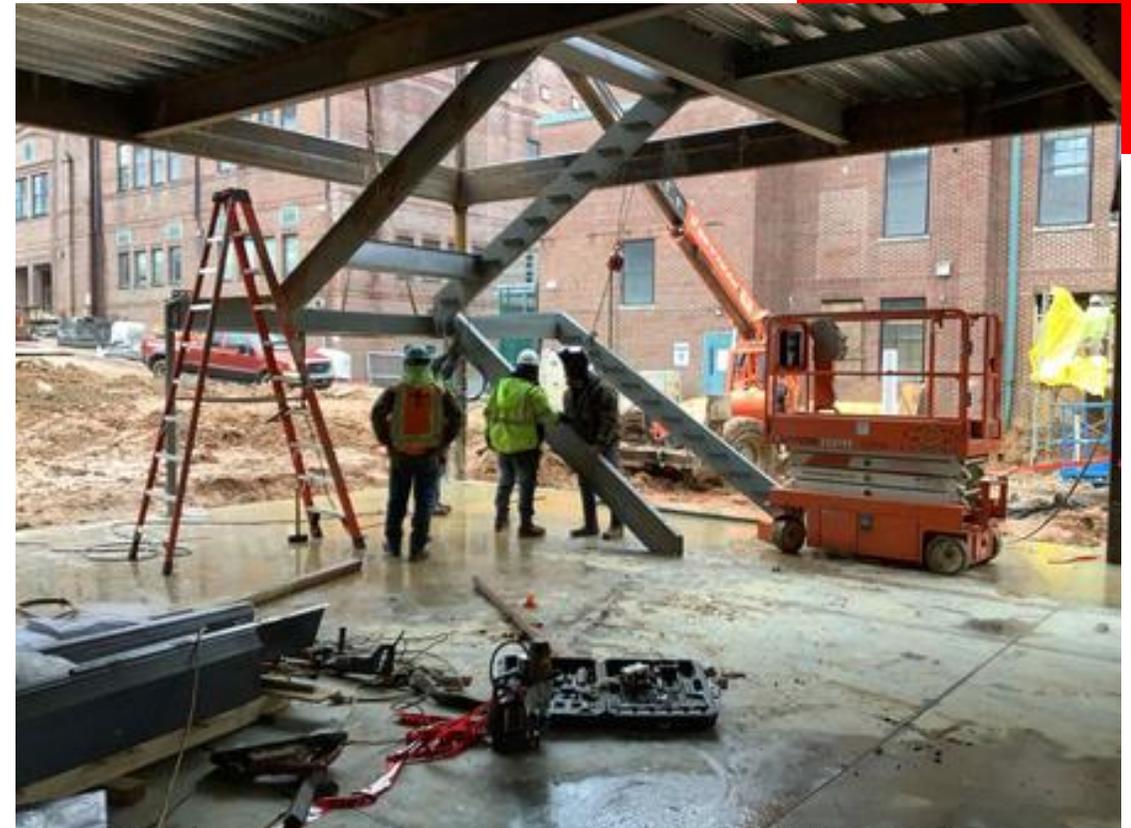

Stair installation at new addition



# Photo/Activity Updates

Media center ceiling grid and paint



Mezzanine HVAC

