



# Weekly Construction Progress Report

## Morningside Elementary School

Week Ending: 01/28/2022

### THIS WEEK

- Mechanical and electrical rough-in continues in Area B and Area D
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation continues
- Hard ceiling installation continues
- Interior painting continues in Area A and Area B
- Steel erection continuing at new addition
- Bridge steel being erected
- Replacement of standing seam metal roof continuing
- Curtainwall clips being installed
- Parapet framing beginning
- Roof decking install continuing
- Cafeteria patio stairs installed
- Plumbing carriers installation beginning
- Exterior metal stud installation beginning

### NEXT WEEK: 01.31.22 – 02.04.22

- Mechanical and electrical continues in Area B and Area D
- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation continues
- Hard ceiling installation continues
- Interior painting continues in Area A and Area B
- Steel erection continuing at completing
- Bridge steel erection completing
- Steel detailing beginning
- Replacement of standing seam metal roof continuing
- Curtainwall clips install continuing
- Parapet framing continuing
- Roof deck install finishing
- Plumbing carriers installation completing
- HVAC rough-in at new addition beginning

### BUDGET/SCHEDULE

#### Construction Budget

\$17,600,000.00

#### Budget Status

\$8,839,447.43

#### Substantial Completion:

July 25, 2022

#### Schedule Status:

On Schedule

Completed By:

Chris Hubbard

**PARRISH**  
CONSTRUCTION GROUP

# Photo/Activity Updates



New addition structural steel



Bridge steel install

# Photo/Activity Updates

New addition stair install

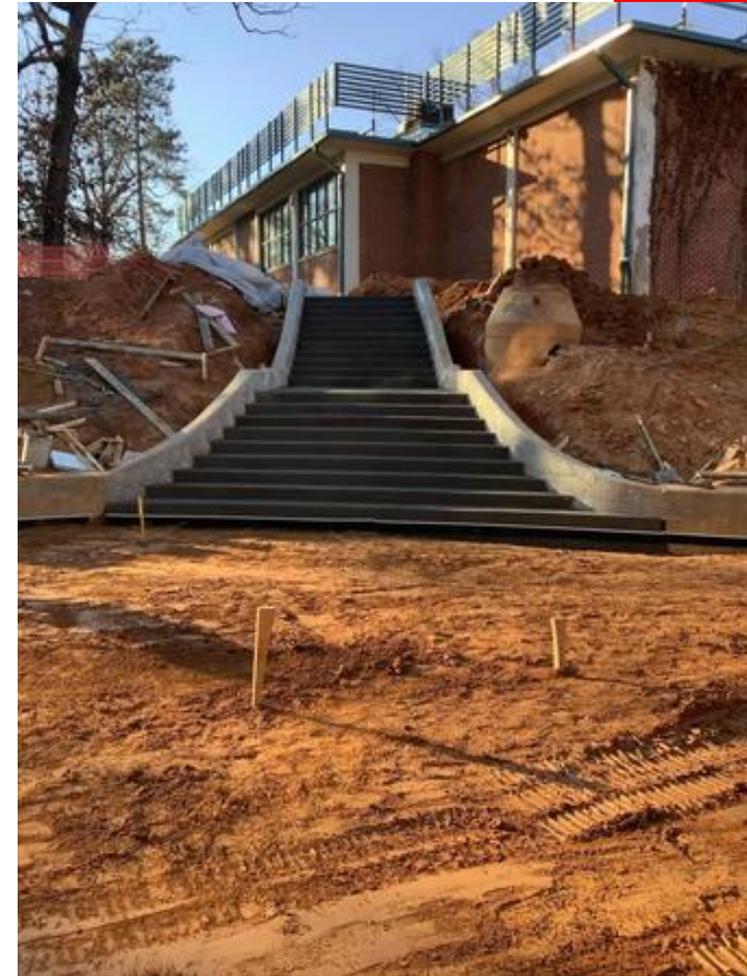
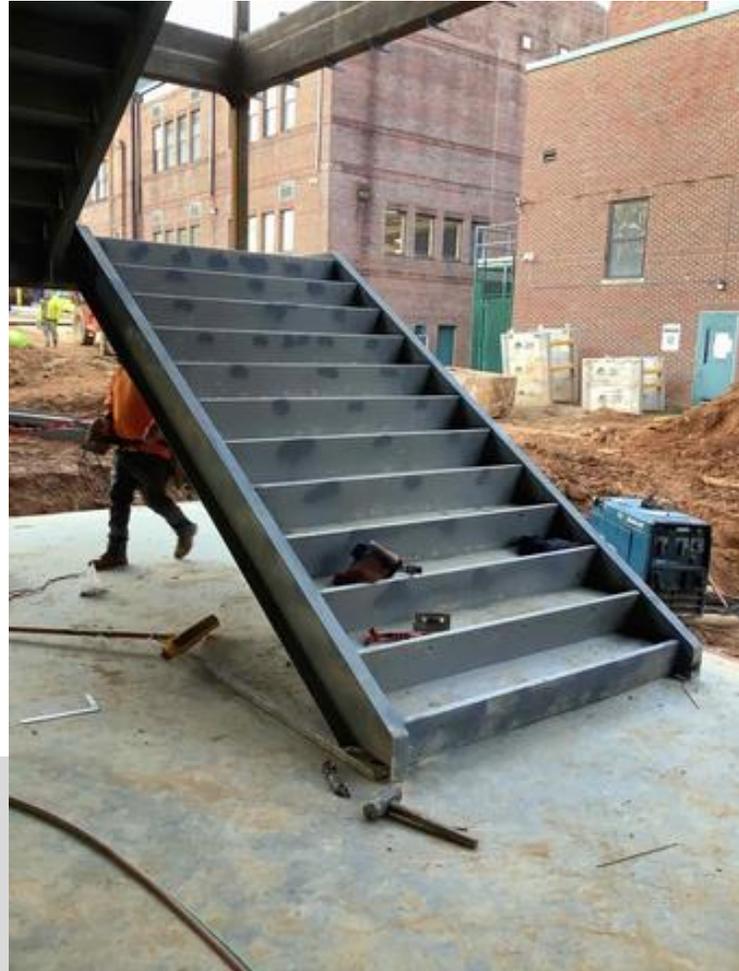


Courtyard stair install



# Photo/Activity Updates

Plumbing carrier install

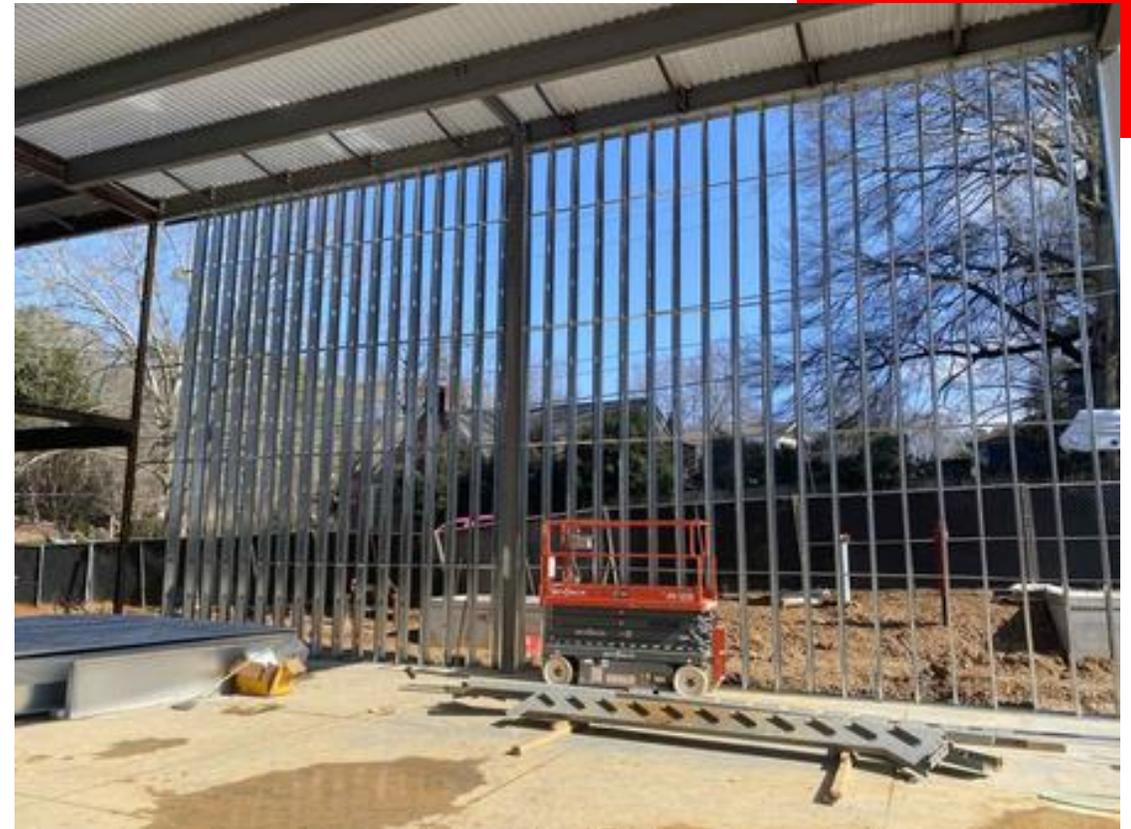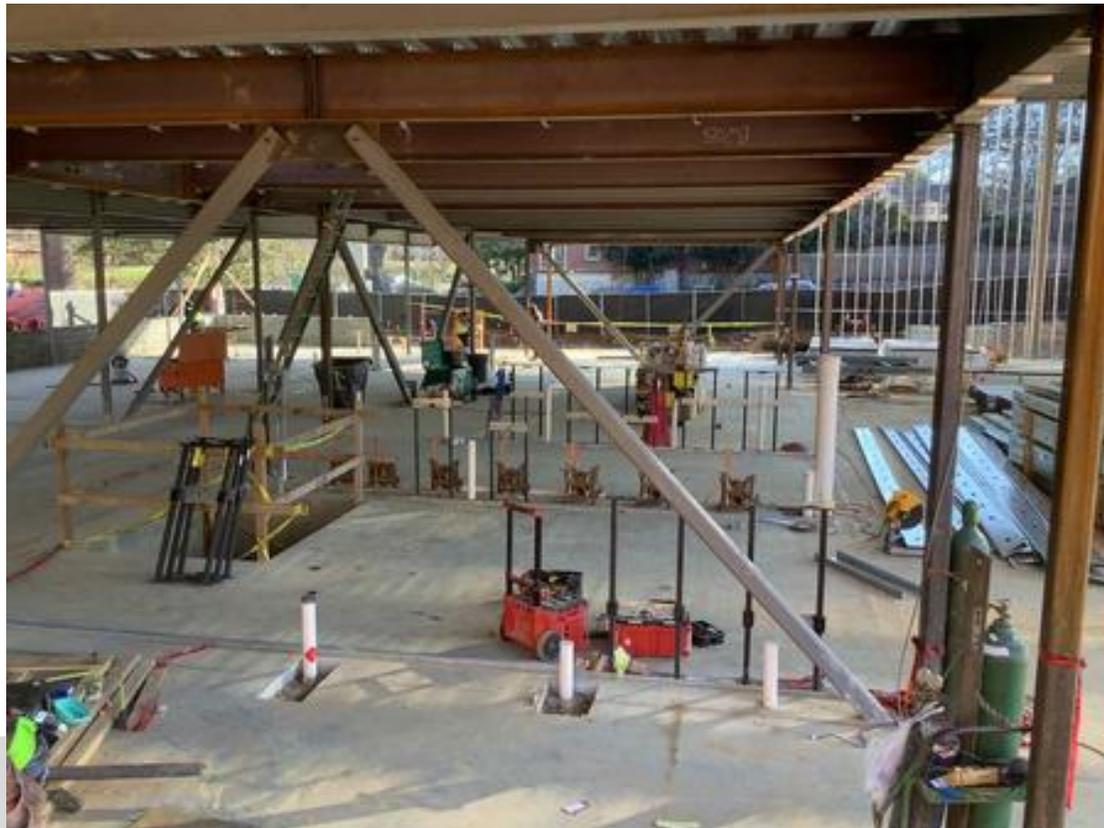

Exterior stud install



# Photo/Activity Updates

Media center paint



Restroom hard ceiling install

