



Weekly Construction Progress Report

Morningside Elementary School

Week Ending: 02/11/2022

THIS WEEK

- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation continuing
- Interior painting continues in Area A, B and D
- Parapet steel continuing
- Replacement of standing seam metal roof continuing
- New addition stairs installation beginning
- Cafeteria curtainwall installation beginning
- New addition curtainwall continuing
- Plumbing carriers and rough-in continuing
- Exterior metal stud installation continuing
- Exterior sheathing beginning
- New addition interior metal stud installation
- New addition HVAC rough-in

NEXT WEEK: 02.14.22 – 02.18.22

- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation continues
- Interior painting continues in Area A and Area B
- Steel detailing continuing
- Replacement of standing seam metal roof continuing
- Parapet framing continuing
- New addition stair installation continuing
- Plumbing carriers and rough-in continuing
- HVAC rough-in at new addition continuing
- Cafeteria curtainwall installation continuing
- New addition interior metal studs
- New addition curtainwall installation continuing
- Topping Out Ceremony

BUDGET/SCHEDULE

Construction Budget

\$17,600,000.00

Budget Status

\$10,263,845.35

Substantial Completion:

July 25, 2022

Schedule Status:

On Schedule

Completed By:

Chris Hubbard

PARRISH
CONSTRUCTION GROUP

Photo/Activity Updates

New addition curtainwall framing




Exterior sheathing install



Photo/Activity Updates

Cafeteria curtainwall

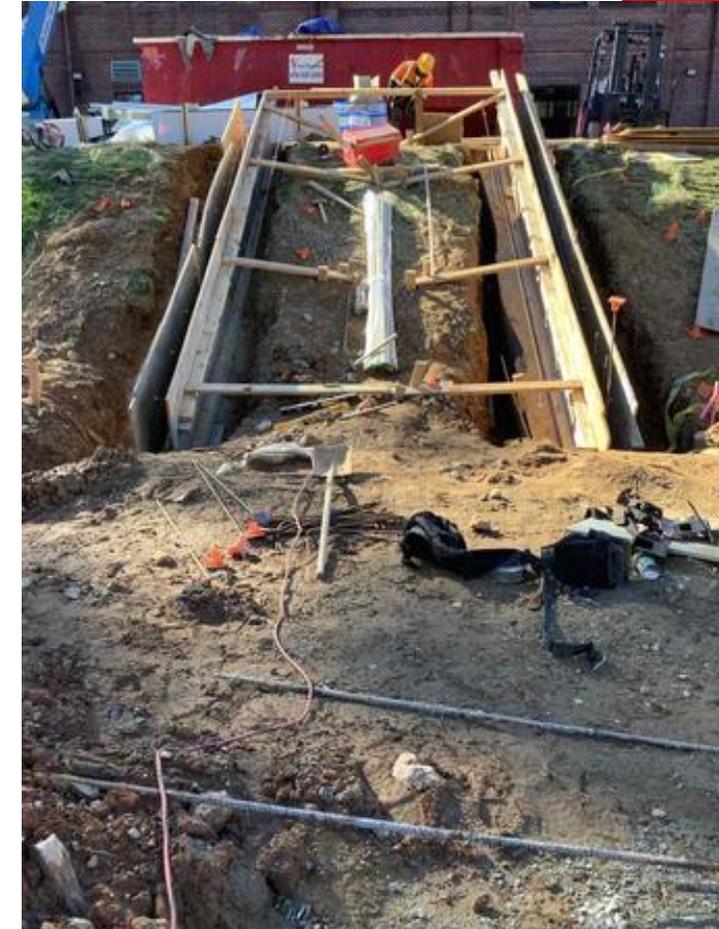

Stair cheek wall install

Photo/Activity Updates

New addition plumbing rough-in



Bridge concrete installed



Photo/Activity Updates

Stairwell paint



Existing building casework install

