



# Weekly Construction Progress Report

## Morningside Elementary School

Week Ending: 03/04/2022

### THIS WEEK

- Sheetrock finishing continues throughout building
- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation finishing
- Interior painting continues in Area A, B and D
- New addition curtainwall continuing
- Plumbing carriers and rough-in continuing
- Exterior metal stud installation continuing
- Exterior sheathing continuing
- New addition interior metal stud installation
- New addition Mechanical , Electrical, & Plumbing rough-in continuing
- Driveway retaining wall install beginning
- Gutter & downspout install at existing COPS building finishes
- Plumbing carriers and rough-in continuing
- Lightweight insulated concrete beginning

### NEXT WEEK: 03.07.22 – 03.11.22

- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Ceiling grid installation continues
- Interior painting continues in Area B, Area B and Area D
- Plumbing carriers and rough-in continuing
- HVAC rough-in at new addition continuing
- New addition interior metal studs continuing
- New addition curtainwall installation continuing
- New addition glass install
- Lightweight insulated concrete roof decking installation beginning at new addition finishing
- Exterior metal stud installation continuing
- Exterior sheathing continuing

### BUDGET/SCHEDULE

#### Construction Budget

\$17,600,000.00

#### Budget Status

\$10,263,845.35

#### Substantial Completion:

July 25, 2022

#### Schedule Status:

On Schedule

Completed By:

Chris Hubbard

**PARRISH**  
CONSTRUCTION GROUP

# Photo/Activity Updates

New addition curtainwall framing



Curtainwall glass delivery



# Photo/Activity Updates

Asphalt primer over decking for LWIC



Insulation for LWIC



# Photo/Activity Updates

GA Power conduit install



Lightweight insulated concrete deck



# Photo/Activity Updates

Demolition of opening for new connecting corridor



Existing cafeteria wall demolition



# Photo/Activity Updates

Can wash concrete install




Driveway retaining wall install



# Photo/Activity Updates

New addition door frame install

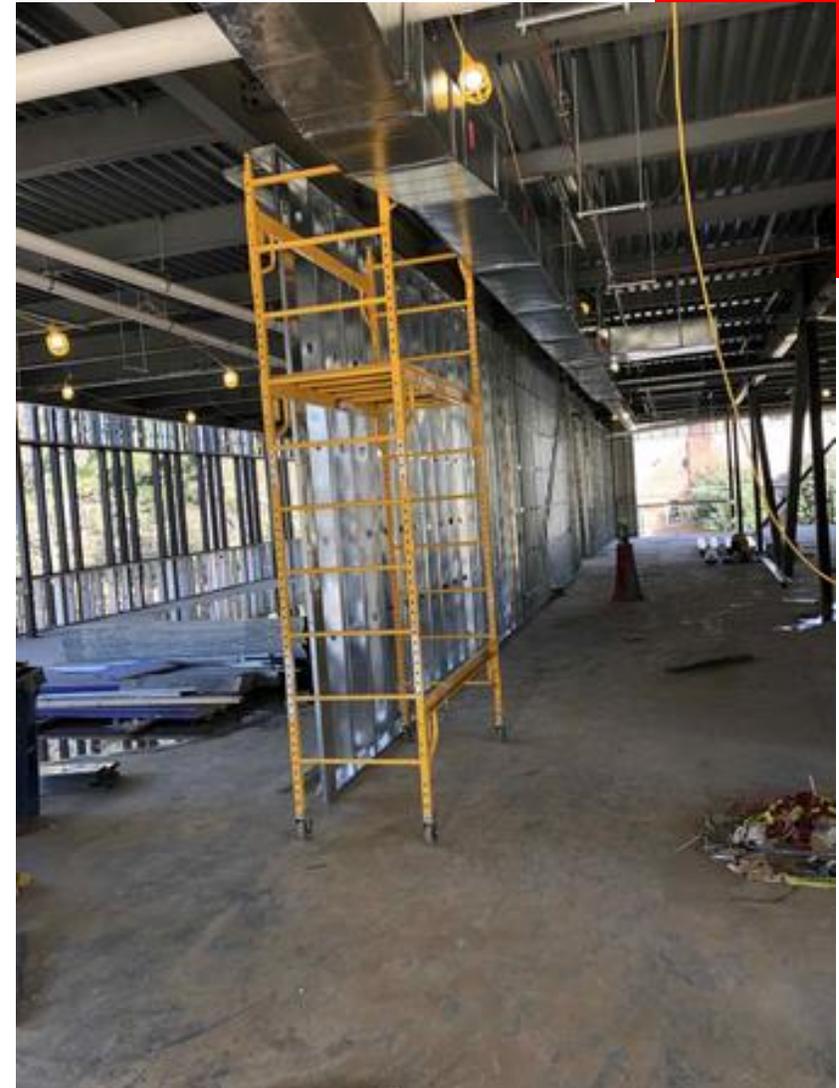

Ductwork and Framing in new addition

