



Weekly Construction Progress Report

Morningside Elementary School

Week Ending: 03/25/2022

THIS WEEK

- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Interior painting continues in Area B and D
- New addition curtainwall continuing
- Curtainwall glass install continuing
- Exterior metal stud installation continuing
- Exterior sheathing continuing
- New addition interior metal stud installation
- New addition Mechanical , Electrical, & Plumbing rough-in continuing
- Driveway retaining wall install continuing
- Steel fireproofing continuing
- New flooring in existing building install
- Drywall installation beginning in new addition
- Can wash and mechanical yard installation
- Epoxy installation beginning

NEXT WEEK: 03.28.22 – 04.01.22

- Fire sprinkler installation continues
- Lighting installation continues in Area B and Area D
- Interior painting continues in Area B and D
- HVAC rough-in at new addition continuing
- New addition electrical continuing
- New addition interior metal studs continuing
- New addition curtainwall installation finishing
- New addition glass install continuing
- Exterior metal stud installation continuing
- Exterior sheathing finishing
- Exterior damp proofing and waterproofing beginning
- Can wash and mechanical yard installation
- Steel fireproofing finishing
- New flooring in existing building install continuing
- Driveway retaining wall install continuing
- Epoxy installation continuing

BUDGET/SCHEDULE

Construction Budget

\$17,600,000.00

Budget Status

\$11,341,552.58

Substantial Completion:

July 25, 2022

Schedule Status:

On Schedule

Completed By:

Chris Hubbard

PARRISH
CONSTRUCTION GROUP

Photo/Activity Updates

New addition curtainwall install



East side glass install



Photo/Activity Updates

West side curtainwall glass install



Exterior damp proofing



Photo/Activity Updates

Electrical rough-in



Mechanical pad concrete



Photo/Activity Updates

Cafeteria drywall install




Epoxy flooring install



Photo/Activity Updates

New kitchen epoxy install

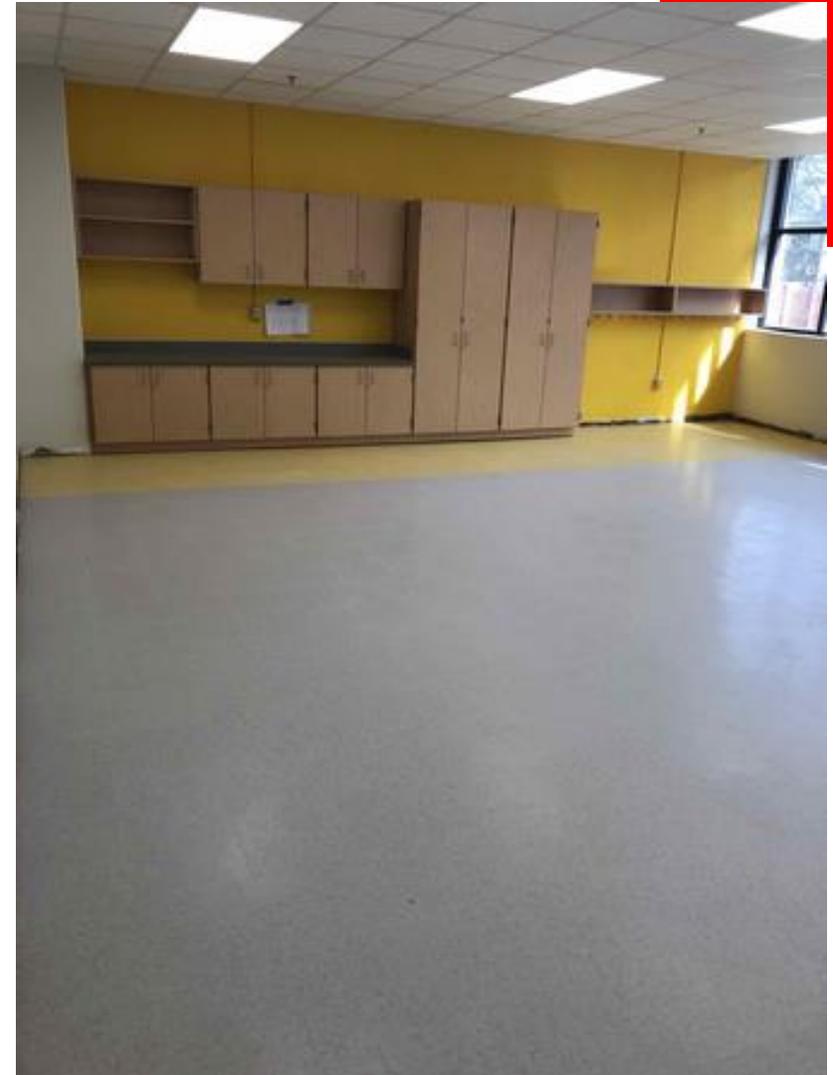

Existing building flooring install

