



# Weekly Construction Progress Report

## Morningside Elementary School

Week Ending: 04/01/2022

### THIS WEEK

- Fire sprinkler installation continuing in Area D
- Mechanical, Electrical, and Plumbing rough-in continuing in new addition
- HVAC Unit installation beginning
- Ceiling tile installation beginning in existing building
- Lighting installation continuing in existing building
- TPO roofing installation beginning
- Metal stud installation in new building continuing
- Drywall installation in new building continuing
- Exterior air barrier installation beginning
- Exterior brick installation beginning
- Storefront framing and glazing installation continuing
- Plumbing fixture installation beginning in the existing building
- Flooring installation continuing in the existing building
- Kitchen epoxy flooring beginning

### NEXT WEEK: 04.04.22 – 04.08.22

- Fire sprinkler installation continuing in Area D
- Mechanical, Electrical, and Plumbing rough-in continuing in the new addition
- Ceiling tile installation continuing in existing building
- Lighting installation continuing in existing building
- TPO roofing installation finishing
- Metal stud installation in new building continuing
- Drywall installation in new building continuing
- Exterior air barrier installation finishing
- Exterior brick installation continuing
- Storefront framing and glazing installation continuing
- Plumbing fixture installation continuing in the existing building
- Flooring installation continuing in the existing building
- Kitchen epoxy flooring finishing
- Metal wall panels clips installation beginning

### BUDGET/SCHEDULE

#### Construction Budget

\$17,600,000.00

#### Budget Status

\$11,341,552.58

#### Substantial Completion:

July 25, 2022

#### Schedule Status:

On Schedule

Completed By:

Chris Hubbard

**PARRISH**  
CONSTRUCTION GROUP

# Photo/Activity Updates

New addition curtainwall install




East side glass install



# Photo/Activity Updates

Exterior air barrier installation

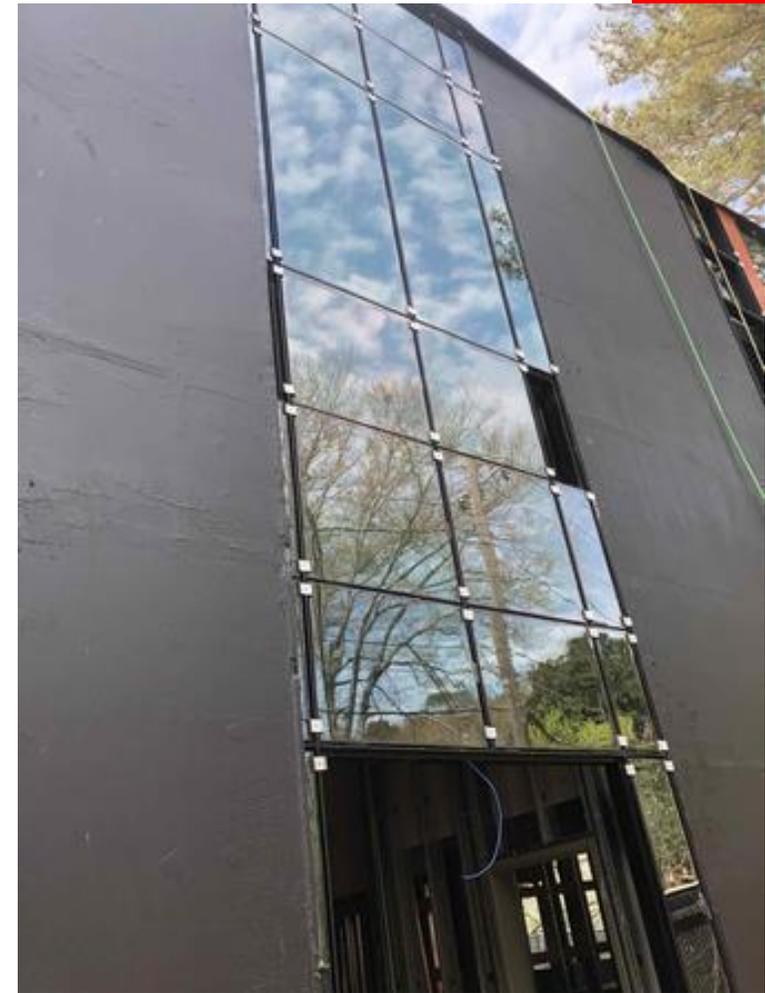

East side storefront install



# Photo/Activity Updates

HVAC units install



Drywall install in new building



# Photo/Activity Updates

Ceiling tile install at existing building



TPO install beginning



# Photo/Activity Updates

Carpet install



Roof access ladder install

