



Weekly Construction Progress Report

Morningside Elementary School

Week Ending: 06/03/2022

THIS WEEK

- Painting continuing in the new building
- Fire sprinkler installation continuing in Area C
- Mechanical, Electrical, and Plumbing rough-in continuing in the new addition
- Lighting installation continuing in new building
- Storefront framing and glazing installation continuing
- Plumbing fixture installation continuing in the existing building
- Flooring installation continuing in the existing building
- Interior handrail installation continuing
- Curb and Gutter installation finishing
- Kitchen equipment installation continuing
- Casework installation continuing
- Metal wall panel installation continuing
- Concrete apron installation finishing
- Gravel installation finishing
- Concrete seat wall beginning

NEXT WEEK: 06.06.22 – 06.10.22

- Painting continuing in the new building
- Fire sprinkler installation continuing in Area C
- Mechanical, Electrical, and Plumbing rough-in continuing in the new addition
- Lighting installation continuing in new building
- Storefront framing and glazing installation continuing
- Plumbing fixture installation continuing in the existing building
- Flooring installation continuing in the existing building
- Interior handrail installation continuing
- Kitchen equipment installation continuing
- Casework installation continuing
- Metal wall panel installation continuing
- Cast stone install beginning
- Sidewalk installation continuing
- Concrete seat wall continuing

BUDGET/SCHEDULE

Construction Budget

\$17,600,000.00

Budget Status

\$14,844,507.37

Substantial Completion:

July 25, 2022

Schedule Status:


On Schedule

Completed By:
Chris Hubbard

PARRISH
CONSTRUCTION GROUP

Photo/Activity Updates

GAB for paving

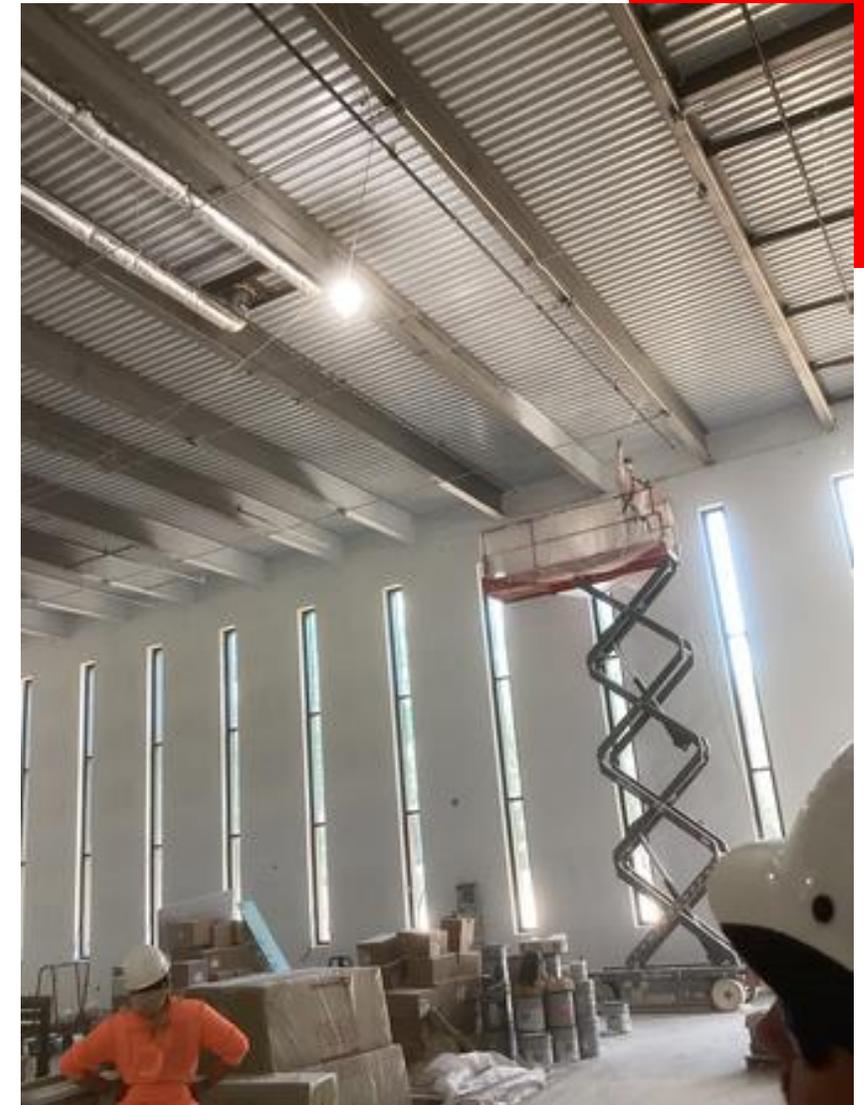

Painting at gym



Photo/Activity Updates

HVAC roof top unit install




New markerboard install



Photo/Activity Updates

Curtainwall Install at gym connector

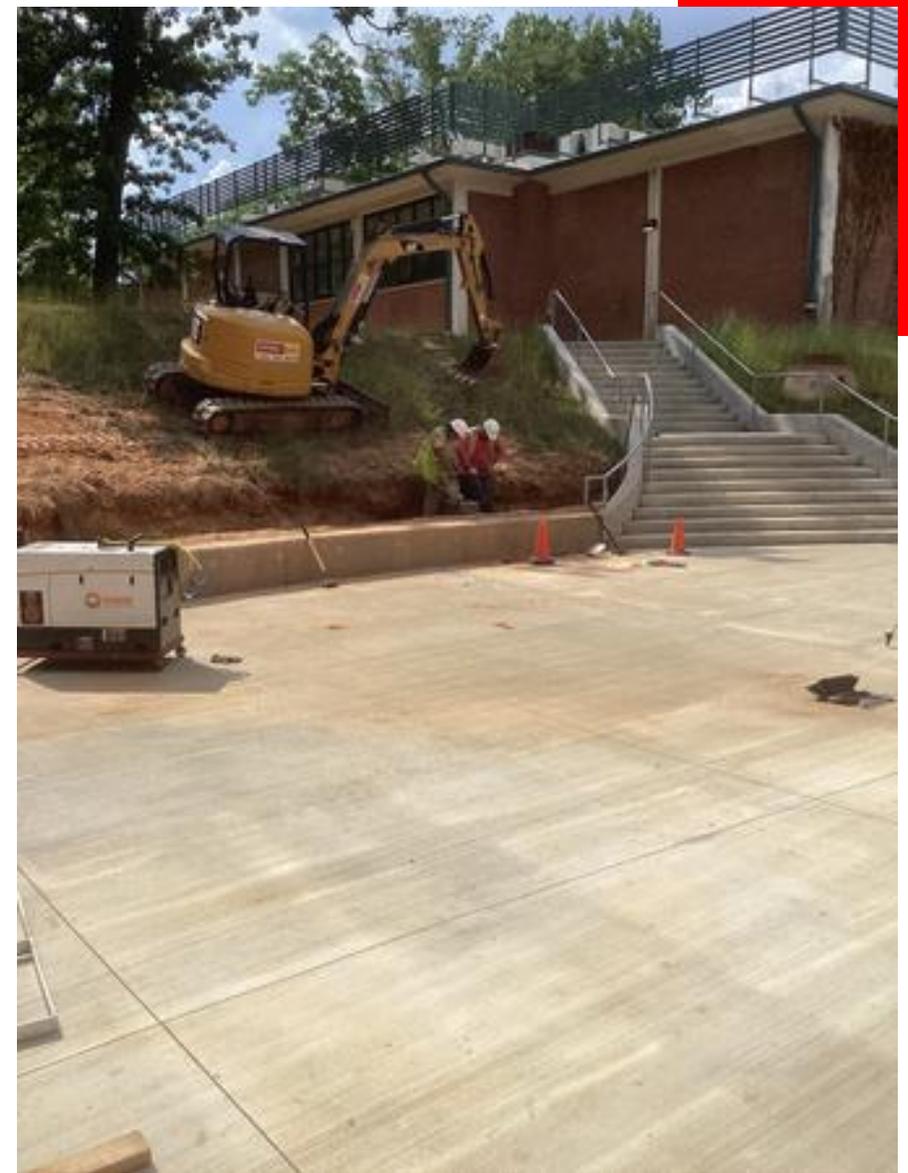

Concrete seat wall install



Photo/Activity Updates



Transformer installation



Kitchen equipment installation

