

## Ongoing Activities

12/31/18 – 01/04/19

- Erecting sequence 2 & 3 steel
- Pour main level east slab on grade
- Installing lower level block walls
- Installing lower level overhead MEP

## Upcoming Activities

- Complete exterior skin mock up
- Continue erecting sequence 2 & 3 steel
- Continue lower level block walls
- Commence installing lower level roofing
- Commence fluid applied air barrier install

## Financial & Schedule Status

Current GMP = \$27.6M  
Bill to Date = \$7,897,109

Start Date: July 2, 2018  
Current Completion Date:  
July 10, 2019

## Project Overview



Photo of the project site from South looking North

## Safety Sector




### “Wet Cutting Masonry”

OSHA recommends using an integrated water delivery system (seen here) on stationary masonry saws, to reduce exposure to silica dust. A pump recirculates the water through a nozzle that directs a continuous stream onto the blade where masonry blocks are being cut, and reduces the dust generated.





Sequence 2 & 3 steel in progress

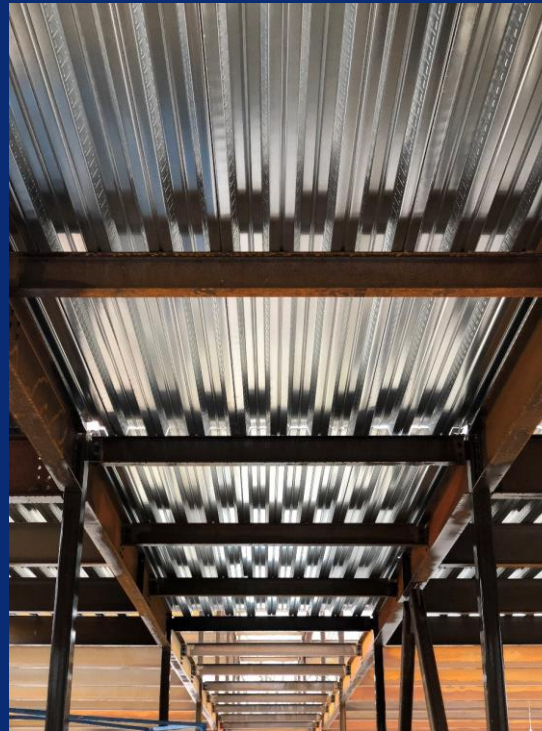

Second level decking being installed



Main level east concrete being installed



Main level east slab on grade  
complete



Interior masonry walls beginning in  
lower level
