

## Ongoing Activities

02/04/19 – 02/08/19

- Erecting sequence 4 & 5 steel
- Prep for lower and main level polished pours
- Framing and sheathing exterior walls on main, 2<sup>nd</sup> and 3<sup>rd</sup> level west
- Installing exterior brick on main, 2<sup>nd</sup> and 3<sup>rd</sup> level west
- Installing main, 2<sup>nd</sup> and 3<sup>rd</sup> level west overhead MEP
- Installing roof 2 (over gym)
- Installing interior framing on main and 2<sup>nd</sup> level west

## Upcoming Activities

- Main and lower level polished area concrete pour
- Finish decking sequence 5 steel
- Painting lower level block walls
- Commence installing roof 3
- Continue framing/sheathing all elevations on west
- Frame interior priority walls
- Metal panel delivery

## Financial & Schedule Status

Current GMP = \$27.6M  
Bill to Date = \$10,797,089

Start Date: July 2, 2018  
Current Completion Date:  
July 10, 2019

## Project Overview



Photo of the project site from sidewalk on Westhaven looking south

## Safety Sector



## “Guardrails”

Openings in the framing have been left to assist in material delivery. Guardrails are in place as the first line of fall protection. Guardrails must consist of a toprail, midrail and toeboard. The toprail must be 42” from the working surface.



## APS Tuskegee Airmen Global Academy

*Project Purpose Statement: To build a new elementary school for Atlanta Public Schools that will create a diverse and innovative learning environment, allowing students' minds to soar.*



Sheathing on main and 2<sup>nd</sup> west



Decking for 2<sup>nd</sup> level east installed



Interior framing on main and 2nd



Eight day time lapse from framing to brick exterior






Interior priority walls receiving GWB



Kitchen, server and faculty dining areas receiving block fill

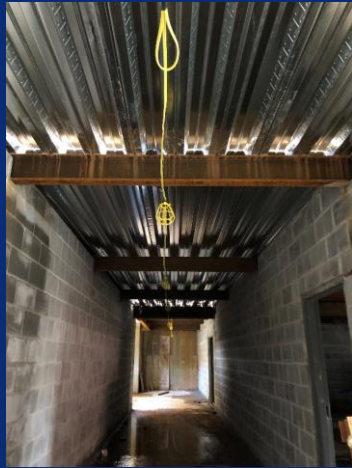

Corridor C3-1 in lower level now covered with decking



Reinforcing install ongoing ahead of concrete pour in polished area

