

CHARLES L. GIDEON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 1/7/19-1/11/19




Balfour Beatty

1/2/19-1/5/19 Activities

- Cover up inspection for in wall at renovation
- Erection of structural steel
- Pour back of interior topping, trenches and SOG
- Several days lost due to 12+ inches of rain between 12/25 and 1/1



Renovation in wall

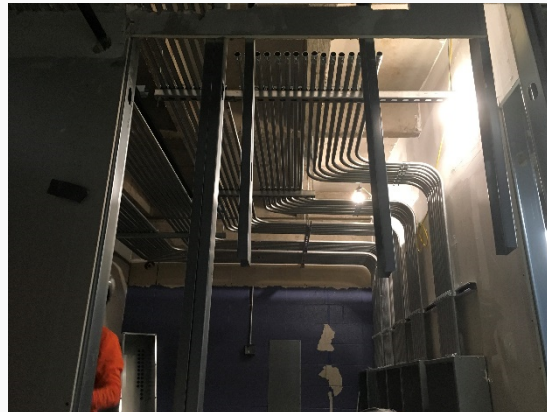

Electrical room OH Rough



Installation HM frames

12/3/18-1/5/19 Activities Continued



SOG pour back at electrical room



Structural Steel Seq 2



Balfour Beatty

1/7/19-1/11/19 Activities

- Pour of lower level SOG and MDF foundation
- Erection of structural steel
- Delivery of new storefront windows and HM for renovation
- 2" topping at rest rooms
- Auditorium MEP rough



Auditorium MEP OH Rough



Interior renovation



2" topping at rest rooms

Balfour Beatty

1/7/19-1/11/19 Activities



Installation of structural steel



Installation of mock up wall

Balfour Beatty



1/14/18-1/18/18 Activities

- Renovation OH rough and classroom and auditorium
- Installation of structural steel sequence 3-4
- Roofing remobilization
- Backfill of retaining wall
- Curb/Gutter and paving

Project Schedule

- Project schedule impacted by delayed LDP and Building Permit procurement
- Project substantial completion: 8/29/19 per 11/20/18 schedule update
 - Upon acceptance of OCO 1 and OCO 2 substantial completion date will change to 8/1/19

Project Financials

- Current contract value: \$14,400,000.

Balfour Beatty
