

CHARLES L. GIDEON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 10/1/18-10/5/18



Balfour Beatty

9/24/18-9/28/18 Activities

- Start of street tie in work
- Interior electrical rough in
- Installation of site utilities
- Mobilize for re-roofing activities



Installation of site utilities



Delivery of roofing materials

Balfour Beatty


10/1/18-10/5/18 Activities



- Sanitary tie in at Welch Street
- Duct installation in existing classroom building
- Re-roofing



Building pad and site New ductwork and re-roof

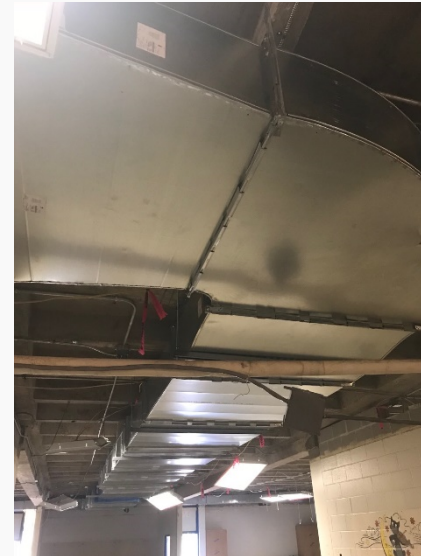

Balfour Beatty

10/1/18-10/5/18 Activities Continued



Sanitary tie in at Welch Street

Balfour Beatty



10/8/18-10/12/18 Activities

- APS abatement
- Start site water lines
- Prep and survey for foundation start
- Continue with MEP rough and re-roof at the existing buildings

Project Schedule

- Project schedule impacted by delayed LDP and Building Permit procurement
- Project substantial completion: 8/26/19 per 9/18/18 schedule update
- Building permit obtained on 10/4/18 – sub remobilization in progress

Project Financials

- Current contract value: \$14,400.00

Balfour Beatty
