

# CHARLES L. GIDEON ELEMENTARY SCHOOL

Weekly Construction Progress Report  
Week 10/15/18-10/19/18



**Balfour Beatty**


# 10/8/18-10/12/18 Activities



- Prep for hurricane
- Interior MEP rough
- Re-roofing
- Abatement
- Setting of grease traps



Re-roofing and MEP rough

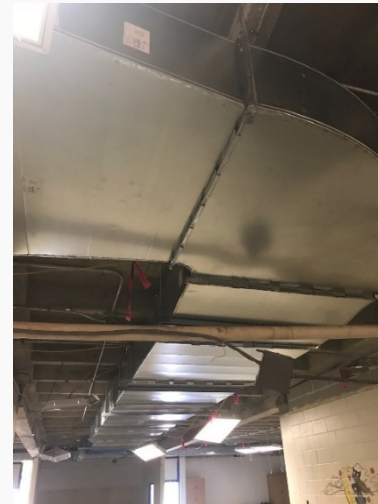

**Balfour Beatty**

# 10/15/18-10/19/18 Activities



- Building survey layout
- Abatement
- Installation of site utilities
- Re-Roofing
- Mobilization and start of retaining wall foundation



Survey Layout and Footing Excavation



Renovation Framing and MEP Rough

**Balfour Beatty**

## 10/15/18-10/19/18 Activities Continued



Retaining wall foundation and rebar

**Balfour Beatty**



## 10/22/18-10/26/18 Activities

- Continue Renovation Rough
- Site Water Lines
- Curb and Gutter
- Rubble Wall at Mary Street
- Retaining Wall and Foundations

## Project Schedule

- Project schedule impacted by delayed LDP and Building Permit procurement
- Project substantial completion: 8/26/19 per 9/18/18 schedule update
- Building permit obtained on 10/4/18

## Project Financials

- Current contract value: \$14,400.00

**Balfour Beatty**
