

CHARLES L. GIDEON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 10/8/18-10/12/18



Balfour Beatty


10/1/18-10/5/18 Activities



- Sanitary tie in at Welch Street
- Duct installation in existing classroom building
- Re-roofing



Building pad and site New ductwork and re-roof

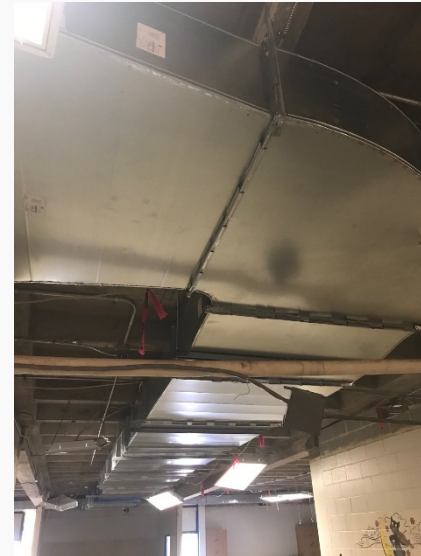

Balfour Beatty

10/8/18-10/12/18 Activities

- Prep for Hurricane Michael impact
- Interior MEP Rough and framing
- Installation of grease traps
- Abatement
- Roofing



Overhead Mechanical Rough In

Balfour Beatty

10/8/18-10/12/18 Activities Continued



Interior Stud Framing



Grease traps

Balfour Beatty



10/15/18-10/19/18 Activities

- APS complete abatement
- Start site water lines
- Start Foundations for retaining wall
- Continue with MEP rough and re-roof at the existing buildings

Project Schedule

- Project schedule impacted by delayed LDP and Building Permit procurement
- Project substantial completion: 8/26/19 per 9/18/18 schedule update
- Building permit obtained on 10/4/18 – sub remobilization in progress

Project Financials

- Current contract value: \$14,400.00

Balfour Beatty
