

# CHARLES L. GIDEON ELEMENTARY SCHOOL


Weekly Construction Progress Report  
Week 11/19/18-11/23/18





**Balfour Beatty**

# 11/12/18-11/16/18 Activities

- Excessive rain shut down exterior activities
- Stripped forms from cast in place wall
- Interior framing and MEP at renovation

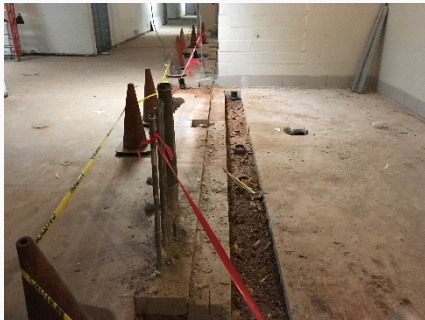

Interior renovation MEP rough and framing / drywall

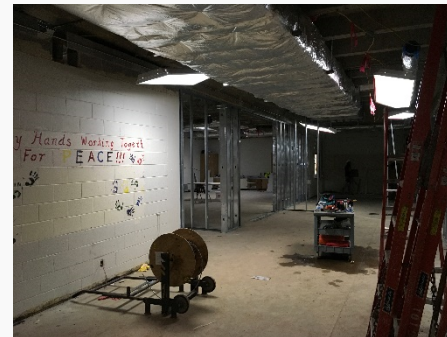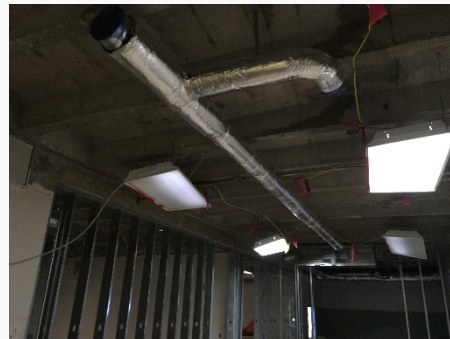

**Balfour Beatty**

# November Aerial Pictures



**Balfour Beatty**  
Construction

Gideons Elementary School

Print #181111077  
Date: 11/11/18  
Lat/Lon: 33.730688 -84.405279  
Order No. 65099  
Aerial Photography, Inc. 954-988-0484



**Balfour Beatty**  
Construction

Gideons Elementary School

Print #181111078  
Date: 11/11/18  
Lat/Lon: 33.730688 -84.405279  
Order No. 65099  
Aerial Photography, Inc. 954-988-0484

**Balfour Beatty**



# 11/19/18-11/23/18 Activities

- Completed Foundations
- Completed curb and gutter
- MEP underground rough at Kitchen
- Interior framing and MEP at renovation
- Closed Thursday and Friday



Stripped Wall



Kitchen underground rough in

**Balfour Beatty**

# 11/19/18-11/23/18 Activities Continued



Elevator Pit Formwork



Curb and gutter

**Balfour Beatty**



## 11/26/18-11/30/18 Activities

- Renovation drywall, sprinkler, in wall inspections
- FW and DW site utilities
- Complete kitchen slab rough
- Binder at parking lot
- Backfill of retaining wall
- Roofing white cap
- Closed for Thanksgiving Holiday

## Project Schedule

- Project schedule impacted by delayed LDP and Building Permit procurement
- Project substantial completion: 8/29/19 per 11/20/18 schedule update

## Project Financials

- Current contract value: \$14,400.00
- Approved OCO 1 \$75,856.45 – Pending execution

**Balfour Beatty**
