

# CHARLES L. GIDEON ELEMENTARY SCHOOL

Weekly Construction Progress Report  
Week 11/5/18-11/10/18



**Balfour Beatty**

# 10/29/18-11/2/18 Activities



- Pour foundations
- Form wall
- Demo auditorium roofing
- Installation of curb and gutter
- Interior framing and MEP at renovation



Installation of Curb and Gutter



Continuous Footing

**Balfour Beatty**

# 10/29/18-11/2/18 Activities Continued



Renovation Framing and MEP Rough

**Balfour Beatty**

# 11/5/18-11/10/18 Activities



- Poured foundations
- Completed forming wall - pour wall Friday (11/9)
- Completed install of grease lines
- Started MEP underground rough at Kitchen
- Interior framing and MEP at renovation
- GP removed overhead power to Gym
- Saturday (11/10) work - Due to rain events this week



Complete Retaining Wall Formwork



Underground Plumbing Rough



Continuous Footing


**Balfour Beatty**



# 11/5/18-11/10/18 Activities Continued



Sawcut Slabs to Install Plumbing

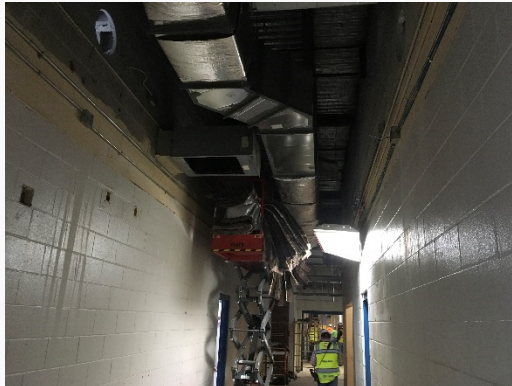

Insulating Duct



Drywall/Framing & MEP Rough

**Balfour Beatty**



## 11/12/18-11/16/18 Activities

- Continue Renovation Rough – LV pending returned submittals
- Continue installing Domestic Water Lines
- Complete foundations
- Complete curb and gutter
- Paving
- Continue under slab plumbing at kitchen
- Fire Water Lines

## Project Schedule

- Project schedule impacted by delayed LDP and Building Permit procurement
- Project substantial completion: 8/29/19 per 11/6/18 schedule update

## Project Financials

- Current contract value: \$14,400.00
- Approved OCO 1 \$75,856.45 – Pending execution

**Balfour Beatty**
