

# CHARLES L. GIDEON ELEMENTARY SCHOOL

Weekly Construction Progress Report  
Week 7/30/18-8/3/18



**Balfour Beatty**

## Last Week Summary 7/23-7/27

- Started vertical demolition
- Continued flooring removal
- Finished ceiling tile and HVAC duct removal
- Removed chiller for salvage to APS



Flooring, ceiling tile, and duct removal




Began vertical demolition of building

**Balfour Beatty**

# This Week Activities 7/30-8/3



- Continue vertical demolition at classroom building
- Continue selective demolition in classroom building
- Installed reshoring at failing existing column
- Began selective demolition at auditorium

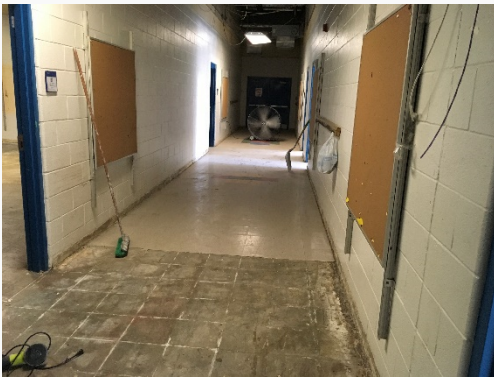

Removal of flooring in classroom building



Vertical demolition



Reshoring of failing existing column

**Balfour Beatty**



## Next Week Activities 8/6-8/10

- Continuation of vertical and selective demolition of buildings
- Installation of erosion control
- Demolition of trailers
- Start of site demolition – Pending LDP

## Project Schedule

- Project substantial completion: 7/18/19 per 8/1/18 schedule update
- Project schedule impacted by delayed LDP procurement

## Project Financials

- Current contract value: \$14,400.00

**Balfour Beatty**
