

CHARLES L. GIDEON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 8/6/18-8/10/18




Balfour Beatty

Last Week Summary 7/30-8/03



- Continue vertical demolition at classroom building
- Continue selective demolition in classroom building
- Installed reshoring at failing existing column
- Began selective demolition at auditorium

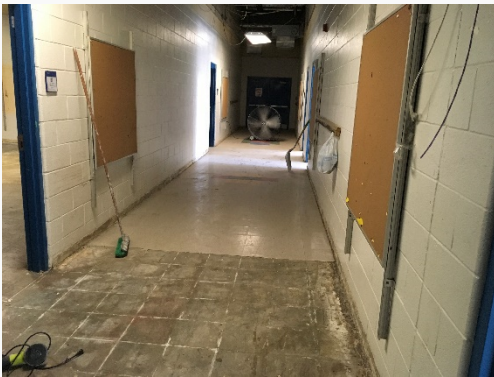

Removal of flooring in classroom building



Vertical demolition




Reshoring of failing existing column

Balfour Beatty

This Week Activities 8/6-8/10



- Continue vertical demolition at classroom building
- Continue selective demolition in classroom building
- Demolition of the interior auditorium space
- Demolition of the trailers

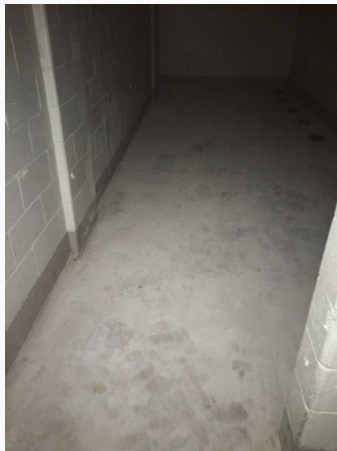

Removal of tile from existing restrooms



Interior demolition of the auditorium



Demolition of the Trailers

Balfour Beatty



Next Week Activities 8/6-8/10

- Continuation of vertical and selective demolition of buildings
- Installation of erosion control – Pending LDP
- Removal of slab on grade
- Start of site demolition – Pending LDP
- Continue interior selective demolition

Project Schedule

- Project substantial completion: 7/18/19 per 8/1/18 schedule update
- Project schedule impacted by delayed LDP procurement

Project Financials

- Current contract value: \$14,400.00

Balfour Beatty
