

EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 10/7/19-10/11/19



Goodwyn, Mills, & Cawood

Balfour Beatty

Current Activities 10/7/19 - 10/11/19

- Installed SPLOST sign at main entrance
- Commencement of abatement at the 2010 building
- Continue demolition at 2021 and 2020 building
- Removed plumbing fixtures to be salvaged
- Commencement of demo of ductwork at the Gym

Upcoming Activities 10/14/19 - 10/18/19

- Continue abatement of floors and begin air sampling
- Commencement of removal of lights at 2010 building
- Commencement of structural demo in 2010 building
- Continue restroom floor tile removal at 2020 and 2021 building



SPLOST Sign Installed at Entrance




Area Contained for Abatement

Activities




Demo of Floors at Gym

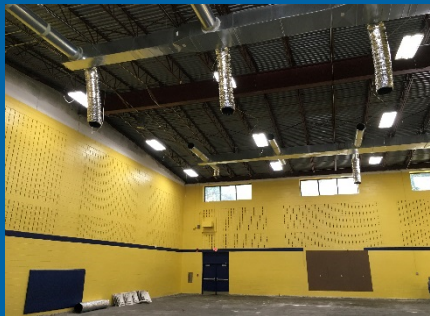


Demo of Ceilings & Overhead
Prep Work at Gym




Demo of Floors, Ceilings, &
Soffits at Media Center

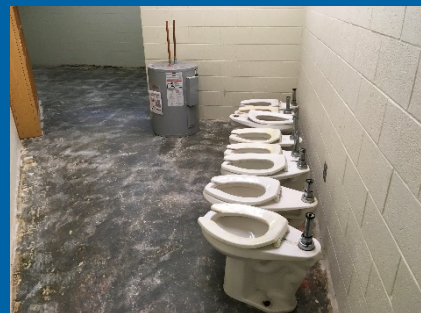

Demo of Existing Toilets

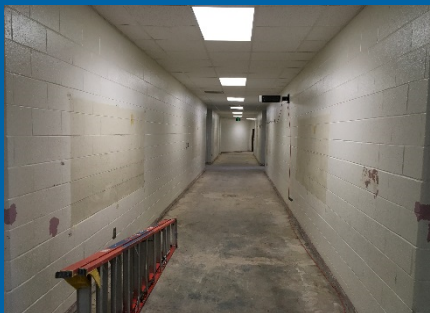

Demo of VCT Flooring at all
Corridors

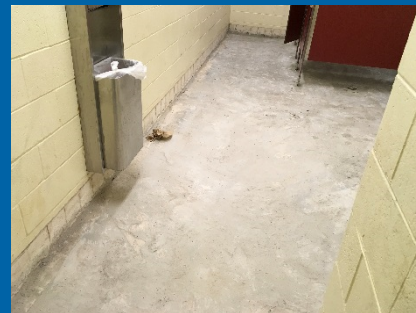

Demo of Quarry Tile at
Restrooms Floors

GMC

Goodwyn, Mills, & Cawood

Balfour Beatty

Project Schedule

- Project Substantial Completion: June 2020 per 10/8/2019 schedule update
- Schedule Status: On Schedule



Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$335,416.92
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
