

# EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report  
Week 12/16/19-12/20/19



Goodwyn, Mills, & Cawood

**Balfour Beatty**

## Current Activities 12/16/19 - 12/20/19

- Patching and pointing-up existing masonry walls.
- Delivered materials for roofing.
- Installing conduit for rough-in of new electrical systems.
- Installed ductwork and VRF systems for new mechanical systems.
- Excavation for new column footings in cafeteria.
- Hung ceiling grid in Bldg. 2010a restrooms.
- Excavation of footing at entrance for underpinning of elevator.

## Upcoming Activities 12/23/19 - 12/27/19

- Continue patching and pointing-up masonry walls.
- Continue demo and reapplication of roofing.
- Begin underpinning for elevator pit.
- Continue installing conduit for rough-in of new electrical systems.
- Continue installing VRF systems for new mechanical systems.
- Continue overhead rough-in of plumbing system.
- Install new drains in courtyard.
- Pour new sidewalks behind gym and in courtyard.



In-fill and Construction of Masonry Walls



Delivery of Roofing Materials

## Activities



Excavation of Footing at  
Entrance for Underpinning



Excavation for New Column  
Footings in Cafeteria.



New Framing, Ductwork, and  
VRF Systems for Offices.

**GMC**


Goodwyn, Mills, & Cawood



Saw Tooting and Removal of  
CMU in Media Center.



Patching of CMU Walls.

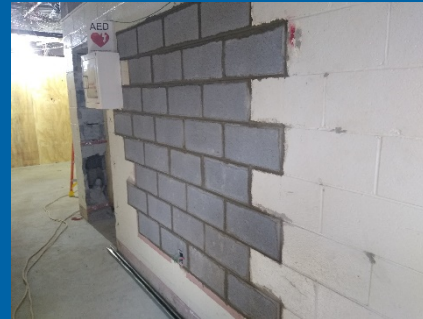

In-fill of Masonry Walls.

**Balfour Beatty**

## Project Schedule

- Project Substantial Completion: June 2020 per 12/17/2019 schedule update
- Schedule Status: On Schedule



## Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$805,272
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
