

EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 2/17/20-2/21/20



Goodwyn, Mills, & Cawood

Balfour Beatty

Current Activities 2/17/20 - 2/21/20


- Demoing and reinstalling roofing at Building 2010
- Installing lights and conduit for classrooms, STEM Lab and kitchen
- Continuing fire alarm rough-in
- Continuing removal and reapplication of exterior window caulking
- Installation of door frames in masonry walls
- Finish masonry plumbing chases
- Demo wall in cafeteria
- Installation of dry wall framing in STEM Lab
- Continue excavation of canopy footings and retaining wall and begin pouring concrete

Upcoming Activities 2/24/20 – 2/28/20

- Continue demo and reapplication of roofing
- Begin replacing metal roof panels
- Install new RTU
- Continue fire alarm rough-in
- Continue electrical rough-in in STEM Lab.
- Continue canopy footing and retaining wall excavation and concrete pours
- Finish installing steel supports in cafeteria
- Continue painting at Building 2020
- Begin installing epoxy flooring in kitchen




Finish masonry plumbing chases

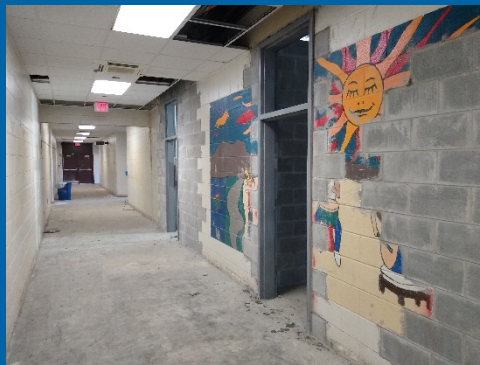

Installation of Door Frames in Masonry Walls

Activities

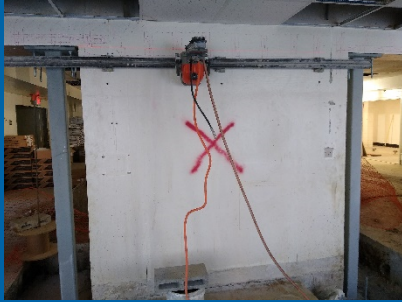

Begin Demo of Wall in Cafeteria



Install New Lighting in Kitchen



Continue Framing and Electrical
Rough-in at STEM Lab

GMC

Goodwyn, Mills, & Cawood

Balfour Beatty

Project Schedule

- Project Substantial Completion: June 2020 per 02/11/2020 schedule update
- Schedule Status: On Schedule



Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$2,362,281
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
