

# EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report  
Week 3/16/20-3/20/20



Goodwyn, Mills, & Cawood


**Balfour Beatty**

## Current Activities 3/16/20 - 3/20/20

- Continuing low voltage and fire alarm rough-in and install new fire alarm devices
- Continue replacing metal roof panels
- Continue roof demo and replacement at building 2010
- Finish epoxy floors in stair well and restrooms
- Pour entry slab and stair
- Relocate power pole, pour new ADA ramp cheek wall, and backfill at ADA ramp.
- Finish duct work at entry
- Form generator pad and pour footings for canopy
- Install ceiling grid in 2010A corridor
- Install ceiling grind at STEM Lab
- Continue painting at building 2020

## Upcoming Activities 3/23/20 – 3/27/20

- Continue demo and reapplication of roofing
- Continue low-voltage and fire alarm rough-in and device installation
- Continue canopy footing and retaining wall excavation and concrete pours
- Begin install of VCT at building 2021
- Begin install of tile in bathrooms in 2021
- Pour entry stairs
- Pour exterior retaining walls at entry

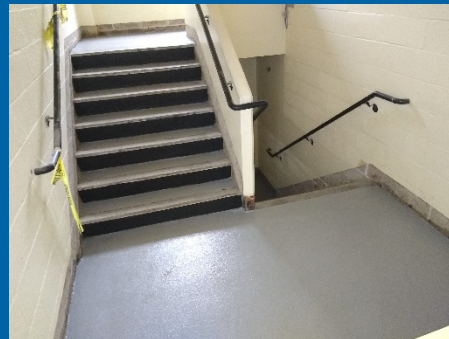

Finish epoxy floors in stair well and restrooms



Install ceiling grid in 2010A corridor

## Activities



Relocate Power Pole and Begin  
Backfill at ADA Ramp



Form and Pour Generator Pad



Form and Pour Entry Walls

**GMC**

Goodwyn, Mills, & Cawood

Insert Text

Insert Text

Insert Text

**Balfour Beatty**

## Project Schedule

- Project Substantial Completion: June 2020 per 03/11/2020 schedule update
- Schedule Status: On Schedule



## Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$3,082,225
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
