

# EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report  
Week 3/30/20-4/03/20



Goodwyn, Mills, & Cawood

**Balfour Beatty**

## Current Activities 3/30/20 - 4/03/20

- Continuing low voltage and fire alarm rough-in
- Complete installation of new metal roofing on building 2021
- Complete roof demo and install white cap on roof at building 2010
- Waterproof and backfill at entry retaining walls
- Pour entry upper slab and entry stairs
- Complete ADA ramp retaining wall and canopy footings and pour exterior stair retaining wall
- Lay VCT at building 2020 classrooms and at building 2021 corridor.
- Install tile in restrooms at building 2020


## Upcoming Activities 4/06/20 – 4/10/20

- Continue demo and reapplication of TPO roofing at building 2020
- Continue low-voltage and fire alarm rough-in and device installation
- Pour Loading Dock Ramp
- Continue install of VCT at STEM Lab
- Continue install of tile in restrooms in 2020
- Lay brick for monument sign
- Begin Epoxy floors at building 2010
- Begin 1<sup>st</sup> coat of paint at building 2010
- Install exterior curtain wall system



Goodwyn, Mills, & Cawood

**Balfour Beatty**

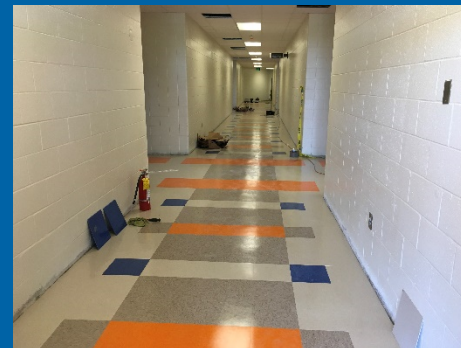

Lay VCT at Building 2020 Classrooms and at Building 2021 Corridor



Form and Pour Entry Stair

## Activities



Pour Upper Entry Slab



Complete ADA Ramp Retaining  
Wall and Canopy Footings



Form and Pour Exterior Stair  
Retaining Wall

**GMC**


Goodwyn, Mills, & Cawood



Complete Installation of White  
Cap at Building 2010B



Complete Installation of White  
Cap at Building 2010A

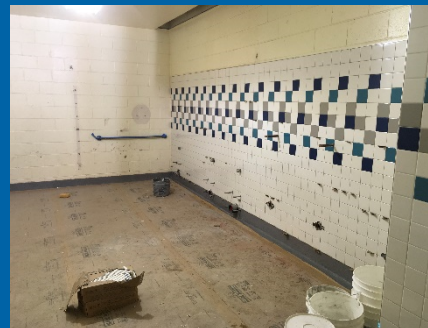

Complete Tile at Building 2021  
Restrooms

**Balfour Beatty**

## Project Schedule

- Project Substantial Completion: June 2020 per 03/24/2020 schedule update
- Schedule Status: On Schedule



## Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$3,082,225
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
