

EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 4/06/20-4/10/20



Goodwyn, Mills, & Cawood

Balfour Beatty

Current Activities 4/06/20 - 4/10/20

- Install support steel in Cafeteria
- Complete installation of new metal roofing on building 2020
- Continue install of white cap on roof at building 2010
- Pour entry upper slab and entry stairs
- Backfill ADA ramp retaining wall and canopy footings and pour exterior stair retaining wall
- Finish VCT at building 2020 classrooms & corridors
- Install tile in restrooms at building 2010
- Apply 1st coat of paint at building 2010
- Finish CMU Wall at Entry
- Pour handicap ramp at entry
- Begin install of tile & epoxy floors at building 2010
- Install new lights in Gym

Upcoming Activities 4/13/20 – 4/17/20

- Continue demo and reapplication of TPO roofing at building 2020
- Pour Loading Dock Ramp
- Finish Epoxy floors at building 2010
- Finish 1st coat of paint at building 2010 classrooms and corridor
- Begin install of exterior curtain wall system
- Begin install of Millwork, Markerboards and Tackboards, and doors at Building 2021




Finish VCT at Building 2020 in Corridors and Classrooms



Apply 1st Coat of Paint at Building 2010

Activities

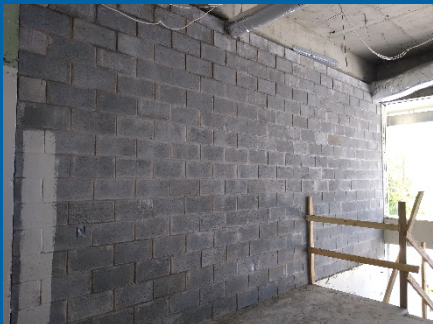

Finish CMU Wall at Entry




Complete Installation of Metal
Roofing At Building 2020




Form and Pour Handicap Ramp at
Entry and Entry Retaining Walls

GMC

Goodwyn, Mills, & Cawood

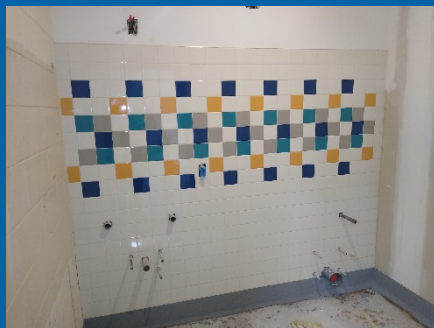

Begin Install of Tile & Epoxy
Floors in Restrooms in 2010

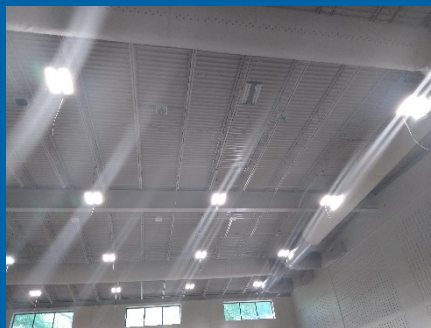

Hang New Lights in Gym



Begin Install of Support Steel in
Cafeteria

Balfour Beatty

Project Schedule

- Project Substantial Completion: June 2020 per 04/07/2020 schedule update
- Schedule Status: On Schedule



Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$4,085,607
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
