

EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 4/27/20-5/01/20



Goodwyn, Mills, & Cawood

Balfour Beatty

Current Activities 4/27/20 - 5/01/20


- Continue install of copings on roof at building 2010
- Replace TPO roof on building 2020
- Pour sidewalks at connector courtyard
- Continue install of ceiling tiles at building 2010
- Complete install of millwork at building 2021
- Complete install of doors at building 2021
- Complete install of toilet partitions in restrooms at building 2021
- Begin install of VCT in 2010 classrooms.
- Install framing for lift shaft at entry
- Remove concrete beam from entry
- Begin pressure washing exterior of building

Upcoming Activities 5/04/20 – 5/08/20

- Continue replacing TPO at building 2020
- Begin install of Bus Loop canopy
- Continue install of millwork at building 2020
- Continue install of doors at building 2020
- Continue install of toilet partitions at building 2020
- Continue install VCT at building 2010
- Install plumbing fixtures at building 2010
- Continue install of ceiling tile at building 2010
- Install glass in Entry curtainwall system
- Drywall lift shaft at entry
- Begin install of accessories at Building 2010



Begin Pressure Wash Building Exterior

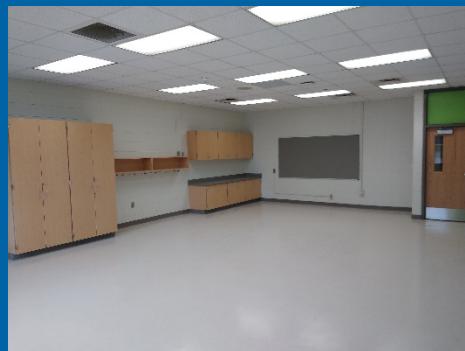

Install Millwork and Cove Base at Building 2021 Classrooms

Activities



Install Toilet Partitions at
Building 2021




Install Doors at Building 2021



Pour Sidewalks at Connector
Courtyard




Goodwyn, Mills, & Cawood

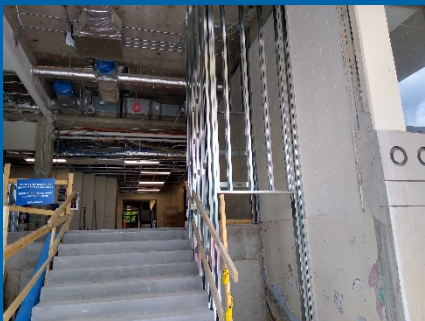

Frame for Lift Shaft and
Removal of Beam at Entry



Begin Install of VCT at Building
2010

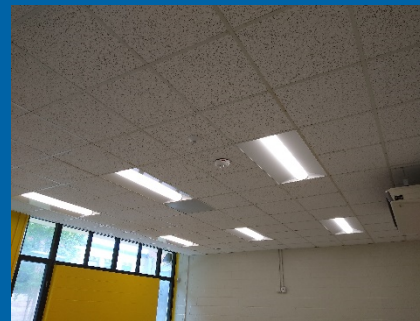

Continue Install of Ceiling Tiles
at Building 2010

Balfour Beatty

Project Schedule

- Project Substantial Completion: June 2020 per 04/21/2020 schedule update
- Schedule Status: On Schedule



Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$4,085,607
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
