

# EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report  
Week 5/11/20-5/15/20



Goodwyn, Mills, & Cawood

**Balfour Beatty**

## Current Activities 5/11/20 - 5/15/20

- Finish install of copings on roof at building 2010
- Continue install of canopy at ADA ramp
- Complete install of storefront and glass at connector
- Begin install of toilet partitions in restrooms at building 2010
- Begin install casework at building 2010
- Apply finish coat of paint in cafeteria and STEM Lab
- Lay VCT in cafeteria and lower level corridor
- Begin install of epoxy flooring on stairs to lower level
- Continue laying VCT at building 2010
- Hang hollow metal doors in corridors and at exterior of building 2021 and 2020
- Hang canopy at loading dock and at building 2020
- Install handrails at loading dock ramp
- Finish drywall and ceiling grid at entry

## Upcoming Activities 5/18/20 – 5/22/20

- Begin install of copings on roof at building 2021
- Complete install of Canopy at ADA ramp
- Complete install of millwork at building 2010
- Begin install of doors at building 2010
- Complete install of toilet partitions at building 2010
- Complete install VCT at building 2010
- Begin install of interior storefront and glass
- Continue install of ceiling tile at building 2010




Complete Install of Storefront System and Glass at Connector



Continue Install of Canopy at ADA Ramp

## Activities

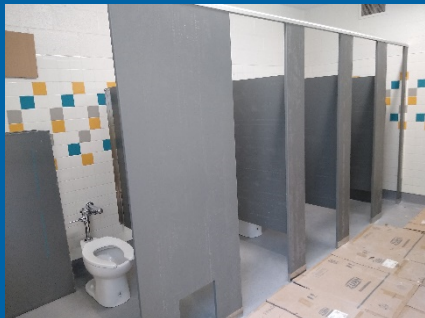

Install Toilet Partitions at  
Building 2010



Begin Install Casework at  
Building 2010




Continue Install of VCT at  
Building 2010



Goodwyn, Mills, & Cawood



Lay VCT and Apply Finish Coat  
of Paint in Cafeteria

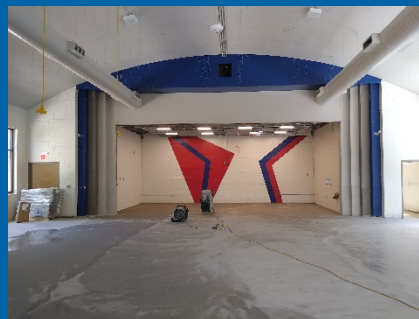

Apply Finish Coat of Paint in  
STEM Lab



Hang Canopy at Loading Dock  
and Install Handrails at Ramp

**Balfour Beatty**

## Project Schedule

- Project Substantial Completion: June 2020 per 05/05/2020 schedule update
- Schedule Status: On Schedule



## Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$5,351,169
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
