

MILES

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 08/25/2025 - 8/29/2025



Balfour Beatty

Current Activities 8/25/2025 - 8/29/2025

- **Complete**
 - MEP investigations
 - Duct Cleaning
 - Gas Pipe Demo
 - LV Demo
 - Tree Trimming
 - Steel Fabrication/Install
- **In Progress - Interior**
 - Interior Demolition - 97%
 - Electrical Reroute
 - ALC scope
 - Ductwork Installation
- **In Progress - Exterior**
 - Roofing Replacement - 90%
 - Helical Piers Installation
 - Roof Hydrants

Key Deliveries

- NG Generator - 12/15/25
- ERUs - 9/26/25




Roof Replacement Progress



Exterior Progress

Progress Photos

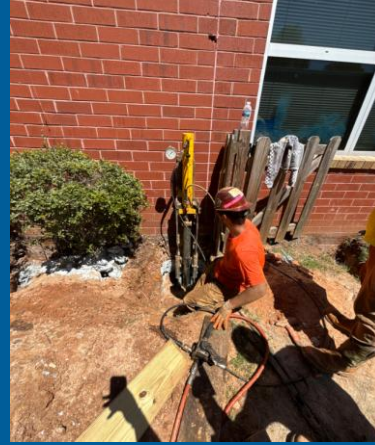

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$10,528,700.00
- Progress Billed to Date: \$2,574,011.28 = 24.45% Completion
- Budget Status: Within GMP

