

# MILES

## ELEMENTARY SCHOOL

*Weekly Construction Progress Report*  
*Week 09/2/2025 - 9/5/2025*



**Balfour Beatty**

## Current Activities 9/2/2025 - 9/5/2025

- **Complete**
  - MEP investigations
  - Duct Cleaning
  - Gas Pipe Demo
  - LV Demo
  - Tree Trimming
- **In Progress - Interior**
  - Interior Demolition - 97%
  - Electrical Reroute
  - Steel Fabrication/Install
  - Ductwork Installation
  - Plumbing Upgrades
- **In Progress - Exterior**
  - Roofing Replacement - 90%
  - Helical Piers Installation
  - Roof Hydrants
  - Exterior Modifications

### Key Deliveries

- NG Generator - 12/15/25
- ERUs - 9/26/25




**Roof Replacement Progress**



**Exterior Progress**

# Progress Photos

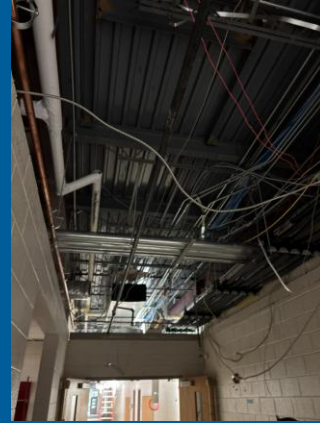

 LORD AECK SARGENT



**Balfour Beatty**

## Project Schedule

- Schedule Status: On Schedule



## Project Financials

- Construction GMP: \$10,528,700.00
- Progress Billed to Date: \$2,574,011.28 = 37.03% Completion
- Budget Status: Within GMP

