

# TOWNS

## ELEMENTARY SCHOOL

*Weekly Construction Progress Report*  
*Week 12/16/2024-12/20/2024*



**Balfour Beatty**

## Current Activities 12/16/2024-12/20/2024


- Complete
  - HVAC Drops in ceilings
- Started/Ongoing
  - APS January Board approval on LV Scope
  - Setting of roof drains at building 2010
  - Demo and Re-roof at building 2010
  - Set roof curbs
  - Return duct at roof curbs
  - Install Roof guardrails
  - Roof coping at building 2011
  - HVAC Controls
  - New Breakers at existing Elec. Panels

## Upcoming Activities 12/23/24-12/27/24


- LED Bulb Retrofit throughout
- Hang Drywall at R.Rooms



**Roofing Activities ongoing**  
**New Controls wire being pulled**

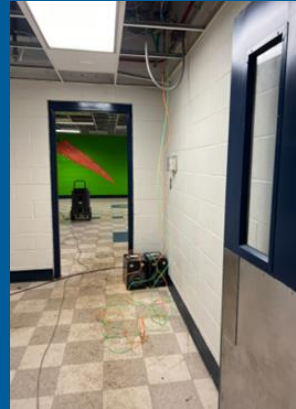

## Progress Photos

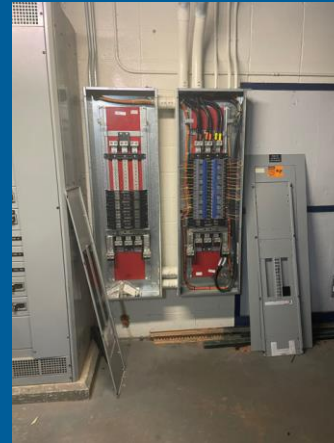

## Project Schedule

- Schedule Status: On Schedule



## Project Financials

- Construction GMP: \$9,500,001.00
- Progress Billed to Date: \$2,457,631.21
- Budget Status: Within GMP

