

# WEST MANOR ELEMENTARY SCHOOL

Weekly Construction Progress Report  
Week 05/17/2021-05/21/2021



**Balfour Beatty**

## Current Activities 05/17/21-05/21/21

- Complete metal panel installation at Gymnasium.
- Continue metal panel installation at entry/admin additions.
- Continue HVAC equipment start-up and testing.
- Continue installation of electrical panels at gymnasium.
- Complete toilet partition and toilet accessory installation at renovation.
- Continue MEP finish trims (outlets, devices, etc.)
- Continue low voltage installation (fire alarm & security) and testing at gymnasium.
- Continue installation of storefront frames and doors.
- Complete installation of markerboards and tackboards.
- Continue installation of gymnasium roof drains and final grade.
- Continue foundations and walls for gymnasium site ramp and stairs.
- Continue MEP overhead drops to grid at gymnasium.
- Complete gymnasium epoxy flooring.
- Complete renovation flooring.
- Start concrete flume at west side of gymnasium.
- Start dumpster screen wall foundations and walls.
- Complete window blind installation in renovation.
- Start interior miscellaneous handrail installation at gymnasium.
- Start/Complete BBC Punch in Renovation (SW Wing, Admin/Media, Kitchen/Cafeteria)

## Upcoming Activities 05/24/21-05/28/21

- Continue HVAC equipment start-up and testing.
- Continue installation of electrical panels at gymnasium.
- Continue MEP finish trims (outlets, devices, etc.)
- Complete low voltage installation (fire alarm & security) and testing at gymnasium.
- Complete installation of storefront frames and doors.
- Continue site ramp/stair foundations and walls.
- Complete MEP overhead drops to grid at gymnasium.
- Complete Drop Ceiling/Cover Up Inspections
- Complete concrete flume at west side of gymnasium.
- Continue dumpster screen wall foundations and walls.
- Start installation of window film at corridor windows and storefront doors.
- Start final clean in renovation.
- Start elevator installation.
- Start plumbing fixture installation at gymnasium.
- Start/Complete BBC Punch in Renovation (North East Wing, North Building (Art and Music)



Gymnasium Southeast Elevation Progress



Gymnasium Site Ramp and Stair Concrete


**Balfour Beatty**



Activities



Dumpster Screen Wall Foundations

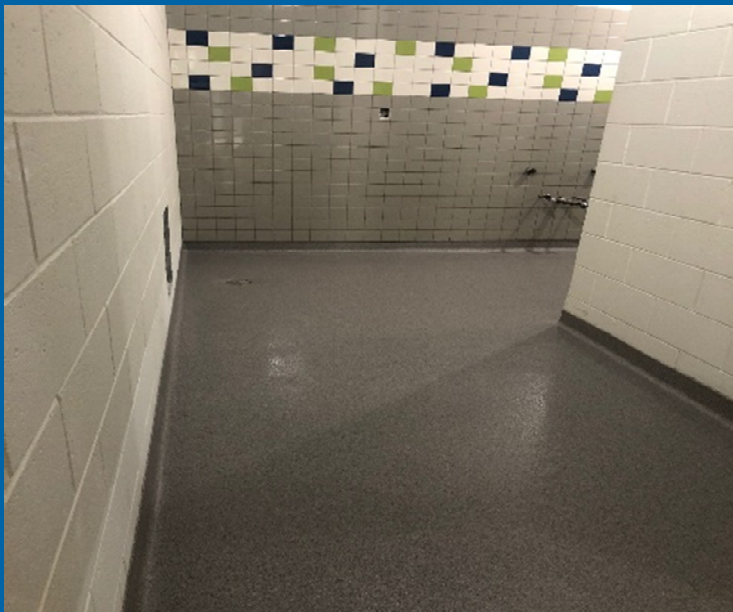

Gymnasium Epoxy Flooring



Gymnasium Ceiling Grid and MEP Drops



Window Blind Installation



Gymnasium Interior Glass and Paint



Admin Addition Metal Panels



## Project Schedule

- Schedule Status: On Schedule



## Project Financials

- Construction GMP: \$11,000,000
- Progress Billed to Date: \$8,375,802
- Budget Status: Within GMP

