

WEST MANOR ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 06/21/2021-06/25/2021



Balfour Beatty

Current Activities 06/21/21-06/25/21

- Continue HVAC equipment start-up and testing.
- Complete MEP finish trims (outlets, devices, etc.)
- Complete final paint at gymnasium/classroom addition.
- Complete VCT/Carpet installation at gymnasium/classroom addition.
- Start/Complete Gymnasium flooring and striping
- Continue gymnasium landscaping and sodding.
- Start/complete place/pour curb and gutter.
- Start final grade around renovation building.
- Continue installation of exterior lighting.
- Continue aluminum canopy installation.
- Continue underground utilities at entrance.
- Set new water utility vaults.
- Start exterior gym ramp and stair railing.
- Continue installation of metal trims/gutters at roof.
- Balfour Beatty Punch List: Interior Gymnasium started 6/23



Gymnasium Sodding and Landscaping



Upcoming Activities 06/28/21-07/02/21

- Complete HVAC equipment start-up and testing.
- Complete aluminum canopy installation.
- Complete rubber base in gymnasium.
- Complete installation of underground water utilities.
- Complete installation of gym ramp and stair railing.
- Complete final grade around renovation.
- Complete installation of trees and grassing.
- Continue roofing metal trim at renovation.
- Complete owner/architect punch list at renovation interior.
- Complete BBC punch list at gymnasium/classroom addition.
- Start asphalt milling and paving.



Gymnasium Flooring and Striping

Activities



Monument Sign Progress



Main Entrance Canopy/Curb Installation




Gymnasium Roof Metal Installation



New Water Vault Installation



Gym/Renovation Final Grade

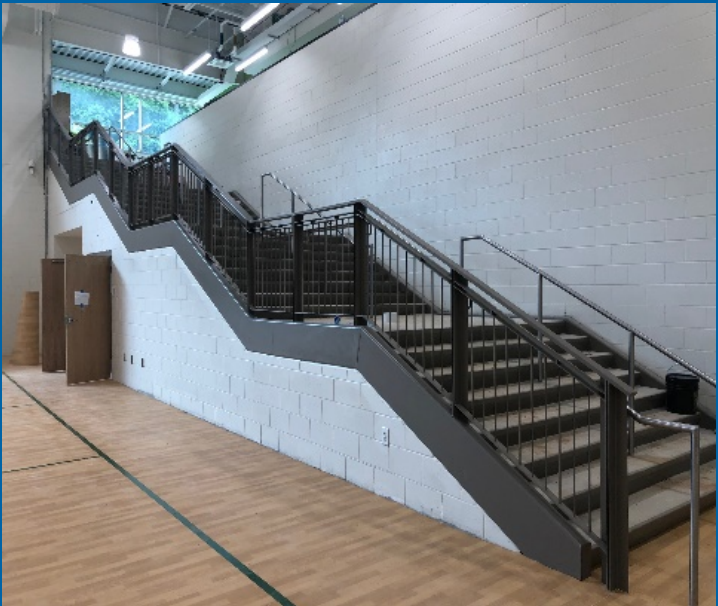

Monument Stair Rail Installation and Paint

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$11,000,000
- Progress Billed to Date: \$9,314,795
- Budget Status: Within GMP

