

WEST MANOR ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 12/7/20-12/11/20



Balfour Beatty

Current Activities 12/7/20-12/11/20

- Continued rebar/concrete at gymnasium addition footings.
- Continued rebar and formwork at gym retaining walls.
- Continued concrete foundation wall pours.
- Continued MEP overhead rough at SW wing of renovation.
- Continued in-wall MEP rough at Renovation.
- Completion of slab pour backs and admin addition SOG.
- Continued waterproofing at gymnasium foundation walls.
- Start MEP Underground at gymnasium addition.



Continuation of Rebar and Formwork at Gym Area

Upcoming Activities 12/14/20-12/18/20

- Complete placement of rebar and concrete at gym addition footings and retaining walls.
- Complete MEP UG at gym and start prep for SOG.
- Complete MEPF overhead rough-in at SW Wing.
- Continuing MEPF overhead rough-in at cafeteria and admin. Area.
- Continuing in-wall MEP rough at Renovation.
- Continue waterproofing.
- Start foundation wall backfill.
- Start roofing replacement on existing building.
- Start interior metal framing and masonry.



Plumbing Underground start at Gym Area

Activities



Cafeteria OH Installation On-going




Elevator Pit Poured



VRF Piping Complete at SW Wing for Pressure Test



Gym Addition North/East Wall Concrete Pour and Waterproofing

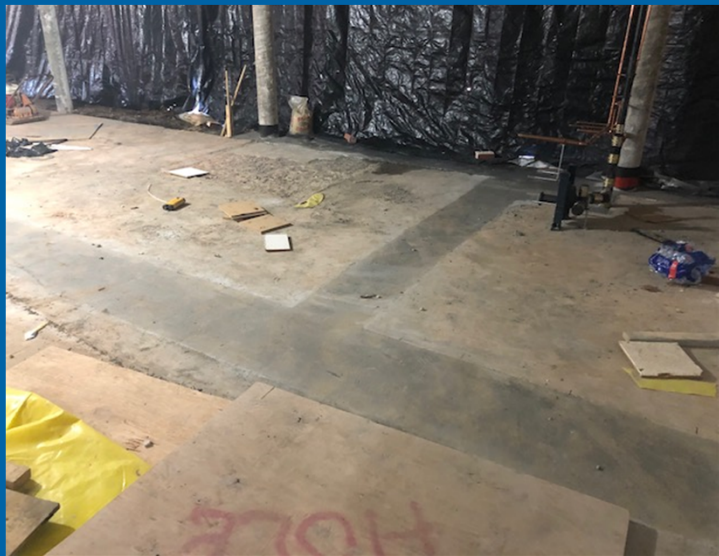

Interior Slab Pour Backs Complete



Admin Addition SOG Complete

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$11,000,000
- Progress Billed to Date: \$1,807,252.77
- Budget Status: Within GMP

