


*Quote of the week: "We all know what giving up feels like. Let's figure out what it feels like if we don't."*

## Project: Bethune CM At Risk Building Improvements

Week Ending: February 10, 2023

### THIS WEEK:

- Installing gas pipe on the roof
- Continuing MEP overhead rough-in
- Frosted glass installation
- Hard ceiling install and finishing
- Continue ceiling grid installation
- Installing Fire Alarm and Intercom
- Installing exterior brick and monument sign

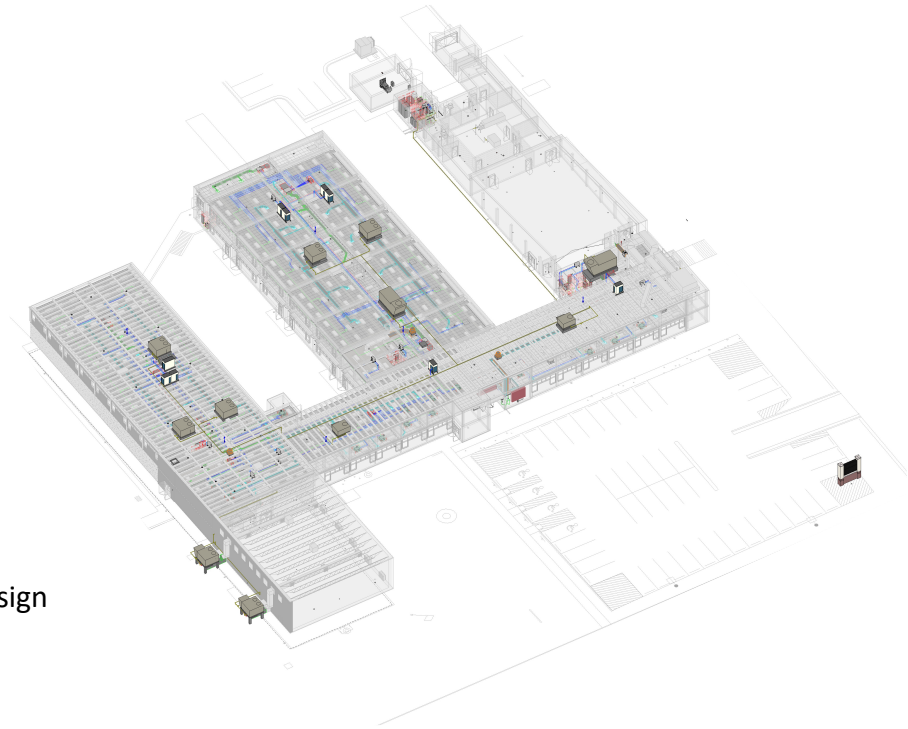

Monument Sign Brick Install



Corridor Ceiling Ceiling Grid Install



Exterior Brick Infill at Cafeteria



Window Frost Film Install



Intercom Device Installation



Corridor Ceiling Grid and Device Installation



**NEXT WEEK** – February 13th through February 17th

- Complete steel reinforcement installation
- Continue with MEP Rough-in
- Continue ceiling grid installation in corridors and remaining classrooms
- Continue installing and finishing hard ceilings

**PAYMENT STATUS:**

- Payment Approved to Date (\$ 2,359,509.73)
- Payment application #4 \$698,190.14 (Pending)

**SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- June 15, 2023

**Final Completion (Not Including New Switchgear)**

- July 11, 2023

**Electrical Switch Gear Completion**

- August 17, 2023

**PREPARED BY:**

Wallace Miles, Carroll Daniel Construction Co.
