


*Quote of the week: "Try to be a rainbow in someone's cloud." — Maya Angelou*

## Project: CW Hill Elementary and Middle School Week Ending: December 5, 2024

### THIS WEEK:

- Continued drywall installation level 2
- Completed waste and vent rough-in walls on level 1 (Everything but the kitchen)
- Plumbing inspection level 1 (Everything but the kitchen)
- Continued plumbing rough-in at the kitchen
- Completed electrical in-wall rough-in level 1
- Continued electrical rough-in overhead level 1, level 2 and in the kitchen
- Electrical in-wall inspection (Wednesday 12-4)
- Installed VRF's in the kitchen
- Completed insulating plumbing overhead and walls on level 2
- Completed framing walls on level 1
- Started framing restroom ceilings on level 2
- Continued VRF line sets in the kitchen

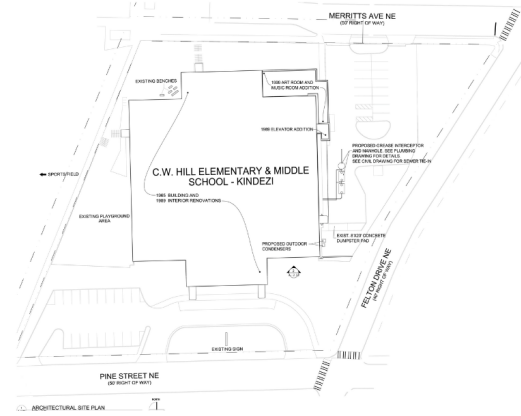

*Stud wall framing in classrooms  
on level 1.*



*Plumbing rough-in and stud  
wall framing in restrooms  
on level 1.*



*Framing ceilings on level 1.*



*Dry wall installation in classrooms on level 2.*

**NEXT WEEK** – December 9th - December 13th

- Continue drywall installation level 2
- Continue plumbing rough-in at the kitchen
- Complete electrical in-wall rough-in level 1
- Continue electrical rough-in overhead level 1, level 2 and in the kitchen
- Continue framing restroom ceilings on level 2
- Continue VRF line sets in the kitchen
- Start hanging drywall level 1
- Complete overhead electrical rough-in level 2

**Final Completion**

- June 30, 2025

**PREPARED BY:**

Orisamola Richardson, Carroll Daniel Construction Co.
