

*Quote of the Week: "The best preparation for tomorrow is doing your best today."*


## Project: CW Hill Elementary and Middle School Week Ending: February 28, 2024

### THIS WEEK:

- Continued painting walls on level 1
- Started hanging drywall for restroom ceilings on level 1 restroom
- Completed light rough-in on level 1
- Completed masonry on level 1 and level 2
- Continued fire sprinkler repair and rough-in on of sprinkler heads on level 1
- Passed inspections for restroom ceilings on level 1
- Started fire alarm rough-in on level 1
- Continued intercom rough-in on level 1 and level 2
- Completed ceramic tile installation on level 1 and level 2
- UDS was delivered this week



*Installing CMU and a door frame in the corridor on level 2.*

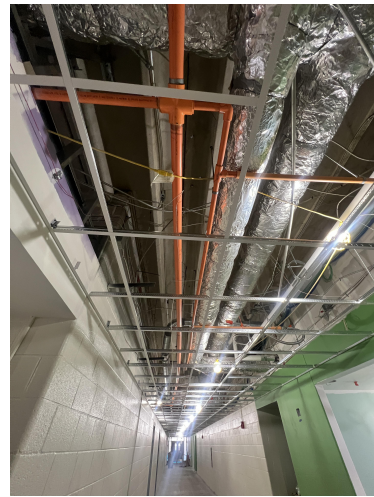

*Installing ceiling grid in the administration office on level 2.*



*Installing ceramic tiling in restrooms on level 1.*



*Painting in the kitchen on level 1.*

### **NEXT WEEK – March 3rd - March 7th**

- Continue painting walls on level 1
- Continue hanging drywall for restroom ceilings on level 1 restroom
- Continue fire sprinkler repair and rough-in on of sprinkler heads on level 1
- Continue fire alarm rough-in on level 1
- Continue intercom rough-in on level 1 and level 2
- Set UDS
- Complete installing ceiling grids on level 2
- Start installing ceiling grids on level 1
- Set generator

### **Final Completion**

- June 30, 2025

### **PREPARED BY:**

Orisamola Richardson, Carroll Daniel Construction Co.
