


Joke of the week: "I told my carpenter I didn't want carpeted steps. He gave me a blank stair."

Project: CW Hill Elementary and Middle School Week Ending: October 25, 2024

THIS WEEK:

- Completed underground plumbing rough in level 1
- Plumbing inspection on level 1 underground plumbing passed
- Continued layout and framing of stud walls on level 2. 95% complete
- Started drywall top out level 2
- Started drywall one side level 2
- Completed waste and vent rough in overhead on level 1
- Plumbing wall & overhead inspections passed
- Continued electrical wall rough in on level 2
- Continued electrical overhead rough in level 2
- Started plumbing trench pour back preparation
- Insulated plumbing inside walls and chases

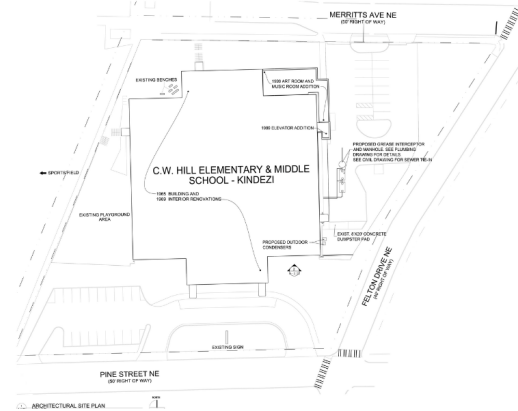

One-sided drywall installation on Level 2.



Plumbing trench pour back preparation on Level 1.



*Plumbing trench pour back
on Level 1.*



*Stud wall framing in classrooms on
Level 2.*

NEXT WEEK – October 28th - October 1st

- Pour concrete pour backs at plumbing trenches
- In wall inspections
- Continue drywall hanging level 2
- Insulate new duct and repair insulation on existing duct
- Plumbing insulation overhead
- Start plumbing wall rough in on level 1
- Complete underground electrical rough in at kitchen
- Pour kitchen slab

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- July 29, 2025

Final Completion

- June 30, 2025

PREPARED BY:

Orisamola Richardson, Carroll Daniel Construction Co.
