


Quote of the week: "The only person you are destined to become is the person you decide to be."

Project: FL Stanton ES Renovation and Addition

Week ending: March 22, 2024

- Continue installing VRF piping and drains
- Continue hanging drywall
- Completed laying brick at the kitchen addition
- Completed hanging duct at the gymnasium
- Media center floor has been poured
- Begin ceramic tile install at all bathrooms
- Set temporary transformer
- Completed all soffit's in the corridor areas
- Continue underground detention pond installation
- Continue plaster repair

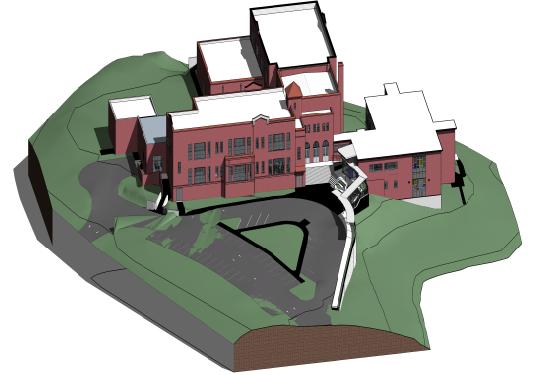

Media Center pour back is complete



Continue to install hollow metal door frames and begin interior paint work



Gym wall is nearing completion, Will begin to apply first coat of paint next week.



Continue with detention pond install

NEXT WEEK – March 25 - March 29

- Begin laying brick at the 1958 wing
- Install cooler freezer
- Begin laying brick at the new monument sign
- Set rooftop units
- Demo school sign
- Frame the ramp and stairs at the gymnasium

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30 , 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
