


Quote of the week: "If you have the courage to begin , you have the courage to win. Take a leap of faith."

Project: FL Stanton ES Renovation and Addition

Week ending: May 31, 2024

- Sprinkler system pressure testing is complete
- Continue with miscellaneous electrical rough in
- Complete exterior paint mock up
- Level 2 VCT install is complete
- Begin installing storefront doors and windows at the security vestibule
- Complete site grading in the parking lot
- Continue installing exterior windows

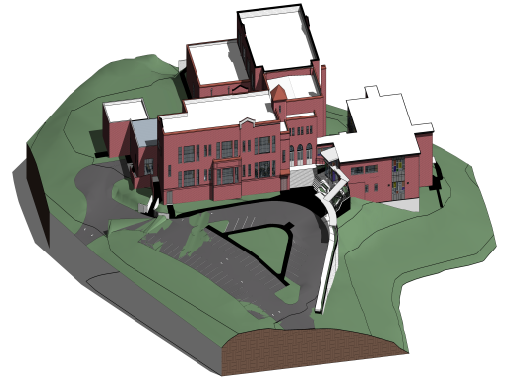

Begin installing toilet accessories and toilet compartments



Resinous flooring in the kitchen is complete



Bathroom resinous flooring is complete



Upstairs level 2 VCT install is complete

NEXT WEEK – June 3 - June 7

- Begin storm water box relocation
- Begin relocating transformer - Georgia Power
- Install generator and generator pad
- Continue with VCT Install
- Continue installing toilet accessories and compartments
- Began installing wall pads in the gym.
- Begin boring to the monument sign
- Begin painting exterior of the building

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30 , 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
