

WEEKLY PROGRESS REPORT – WEEK #012
OWNER: APS

PROJECT MANAGER: MR. BILL ROBINSON

ARCHITECT: SY RICHARDS

GENERAL CONTRACTOR: FS360, LLC

DATES: 6/13/22 – 6/17/22

PM: MR. WILLIAM CALLIER

SUPERINTENDENT: MR. JAMES ENT

Schedule Review:

- Turnover – 7/15/22
- **Major Activities:**
 - Additional change order demo, flooring, finishing, painting, and electrical rough-in
 - Switchgear shutdown and replacement distribution panel tie-in
 - Exterior pressure washing (ongoing)
 - Initial cleaning prep for floor stripping week of 6/20
- **Items to Complete:**
 - Building permitting
 - 100% ceiling cover-up post-inspection
 - Cafeteria lighting delayed by manufacturer (see attached letter). Revised delivery date of 8/24; will follow-up with update.
 - Elevator modernization equipment delayed until early-September by Mowrey Elevator (see attached letter). Will follow-up with contingency plan for installation.
 - Generator still scheduled for early-October delivery & installation per Generac.
- **Misc. Items:**
 - N/A

RFI Log Review:

- RFI Tracking Log/Status:
 - Total RFI's – 5
 - Total Open RFI's - 0

Submittal Log Review:

- Current submittal log:

Spec Section	Title	Status
096723 - Resilient Flooring	Resilient Flooring Samples	Approved
096723 - Resilient Flooring	Resilient Flooring Product Data	Approved
26 32 00 - Emergency/Standby Power Systems Generator Set	Emergency Generator Submittal	Approved
26 05 00 - Basic Materials and Methods	SPD	Approved
26 05 00 - Basic Materials and Methods	Transformer	Approved
26 05 00 - Basic Materials and Methods	Electrical Lighting	Approved

26 05 00 - Basic Materials and Methods	Electrical Panelboards REV.1	Approved
26 05 00 - Basic Materials and Methods	Electrical Panelboards	Approved
26 05 00 - Basic Materials and Methods	Electrical Conduit	Approved
26 05 00 - Basic Materials and Methods	Electrical Wire	Approved
26 05 00 - Basic Materials and Methods	Electrical Access.	Approved
23 81 26 - Ductless Air Conditioners	Mini Split-System AC Product Data	Approved
23 37 13 - Diffusers, Registers, and Grilles	DIFFUSERS, REGISTERS, DAMPERS & FANS	Approved
10 14 00 - Signage	Signage Shop Dwgs	Awaiting Approval
09 90 00 - Painting and Coating	Paint Product Data	Approved
09 51 00 - Acoustical Ceilings	ACT Grid & Tile Product Data	Approved
09 22 16 - Non-Structural Metal Framing	NS Metal Framing Product Data	Approved
09 21 16 - Gypsum Board Assemblies	Gypsum Board Product Data	Approved


- Below submittals forthcoming next week:
- N/A

Pay Application Status:

- Pay Application 001 – Forthcoming

PAY APP NO.	DATE	VALUE	% COMPLETE	Contract Amount	PAID TO DATE:
001	5/3/22	\$268,532.78	28%	\$1,060,066.33	\$268,532.78
002	6/3/22	\$200,453.07	49%	\$1,060,066.33	\$268,532.78
003	N/A	N/A	N/A	\$1,060,066.33	
004					

Photo(s) – 6/17/22:

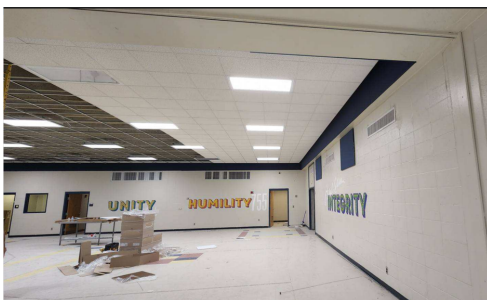

**Acuity Distributor Center
Order Status**

Order #: A435-47389-LLA

Distributor P.O. #: 603JAW1547152

Entry Date: 04-22-2022

Contractor P.O. #: ATLANTA PUBLIC SCHO

Job Name: MAYER / APS Virtual Academy

Bill To: MAYER ELECTRIC SUPPLY PO BOX 5295 PORTLAND, OR 97208-5295

Ship To: B B SERVICES ATLANTA PUBLIC SCHOOLS 20 EVELYN WAY NW ATLANTA, GA 30318-6418

**Alt Ship
To:**

Ship Instr: Call 404-304-4562 24 HRS B4 DEL Contact: RODNEY

Line #	PO Line #	Line Type	Carton Mkg	Type	Shipment #	Catalog Number	Qty	Qty Shipped	Status	Date Type	Date Value	Ship From	Carrier	Pro Number
1.000	1	As Ordered	A1	A1	2	2VRTL G L48 10000LM ICW AP250FL 120 GZ1 40K 80CRI WH	32	32	Shipped	Ship Date	05-18-2022	CONYERS, GA	JCKO	000454704
2.000	2	As Ordered	A1E	A1E	3	2VRTL G L48 10000LM ICW AP250FL 120 GZ1 40K 80CRI PS1050 WH	8	8	Shipped	Ship Date	05-18-2022	CONYERS, GA	JCKO	000454707
3.000	3	As Ordered	C1	C1	0	JCBL 15000LM ACFR MVOLT GZ10 40K 80CRI PM DWHXD	16	0	Not Shipped	Revised Estimated Ship Date	08-24-2022	CONYERS, GA		
4.000	4	As Ordered	C1E	C1E	0	JCBL 15000LM ACFR MVOLT GZ10 40K 80CRI E10WCP PM DWHXD	2	0	Not Shipped	Revised Estimated Ship Date	08-24-2022	CONYERS, GA		
5.000	5	As Ordered			1	SPODM D WH	7	7	Shipped	Ship Date	04-25-2022	CARLISLE, PA	UPS	1Z4E677V034036 5225
6.000	6	As Ordered	EMERGE NCY RELAY	EMER GENC Y RELAY	4	ETS20 DR M20	85	85	Shipped	Ship Date	06-06-2022	DES PLAINES, IL	UPS	1Z643028037982 9978



RE: Equipment Delays

Will,

Due to the ongoing supply chain issues our manufacturing has endured longer than expected lead times for equipment. The current scheduling has the doors and cabs for the APS Virtual Academy Elevator not being manufactured until the first week of September. While we are doing everything we can to expedite materials some things are out of our control. If something changes I will keep you updated.

Thank you,

Tony Glover
Modernization Manager
Mowrey Elevator Company of Fl., Inc.
4518 Lafayette St.
Marianna, Fl. 32446
800-441-4449 x118
