


*Quote of the week: "Decide that you want it more then you are afraid of it."*

## Project: FL Stanton ES Renovation and addition

**Week ending December 15, 2023**

- Pour foundation footings and wall at the new kitchen additions - Complete
- Plumbing inspection on the upper level has been completed
- Continue metal stud framing in the 1928 wing
- Metal stud deck install in the media center is complete
- Continue installing feeders and wire mold in the 1928 wing
- Continue electrical rough - in gym area
- Continue installing door frames on the first level
- Continue constructing CMU walls and block infilling on level 1
- Excavate retaining wall - Complete

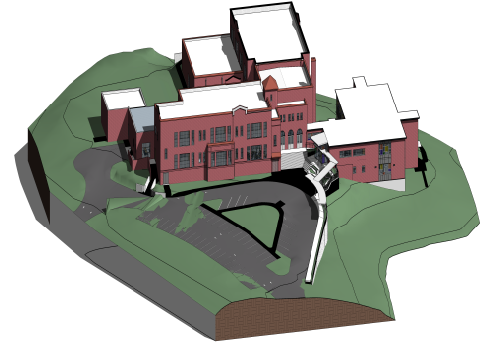

*Media center metal stud deck framing is complete*



*Poured wall for the New Kitchen addition*



*Continue metal stud framing in the  
1928 wing*



*Continue door frame install on level  
1*

## **NEXT WEEK – December 18- December 22**

- Begin Trench pour back in the cafeteria area
- Pour interior slab footing for new kitchen addition
- Begin underground plumbing for new kitchen addition next week
- Continue sprinkler pipe install throughout
- Complete media center floor pour back
- Complete miscellaneous demo
- Begin storm-water system install

## **SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- June 30 , 2024

## **Final Completion**

- June 30, 2024

## **PREPARED BY:**

Jahaziel Lee, Carroll Daniel Construction Co.
