

WEEKLY CONSTRUCTION PROGRESS REPORT

"If you have the courage to begin , you have the courage to win. Take a leap of faith."

Project: Hank Aaron Academy Renovation and Addition


Week ending: 08/23/2024

Review of weekly progress

- Located existing utilities
- Set up construction trailer
- Coordinated with Georgia Power for site lighting
- Coordinated with AGL for reroute of gas for building
- Coordinate site logistics and exterior signs.

Two week look ahead

- Receive LDP
- Erosion control & silt fence install
- Start Phase 1 site demo
- Start mass grading

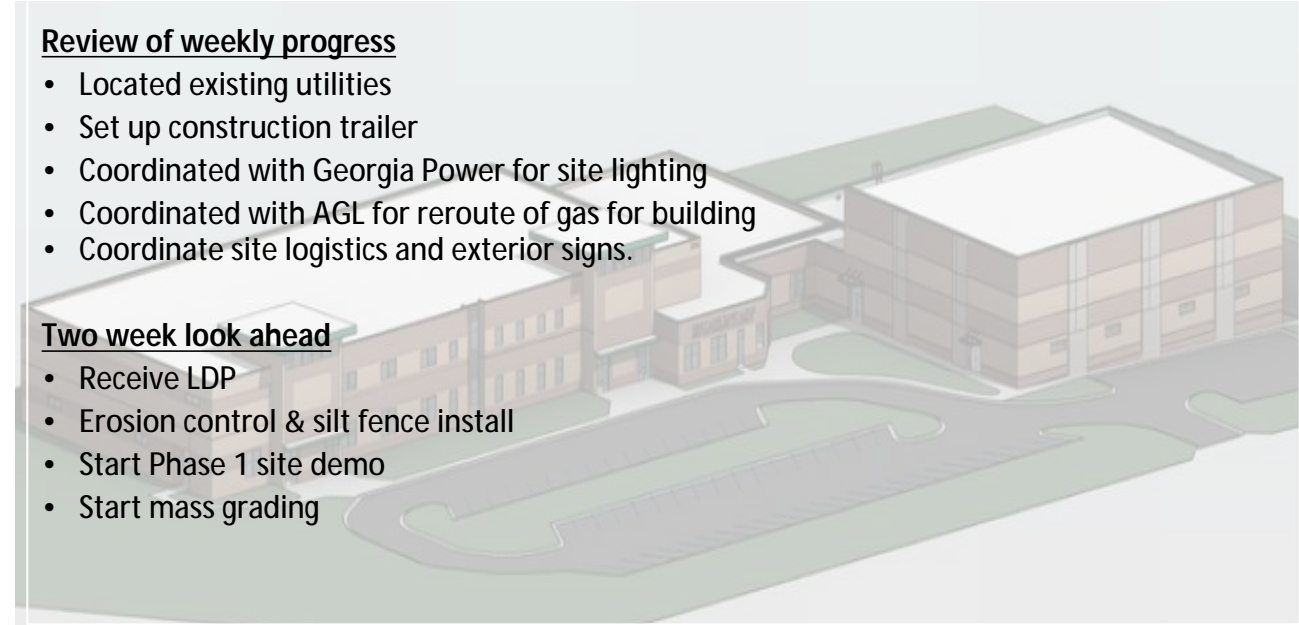

Construction Trailer set up and active



Temp fence and screening installed for Phase 1 of construction



*Construction Trailer being moved
into rear of campus*



Locating and layout of site utilities

Next OAC meeting: Tuesday, September 3rd, 2024

Schedule date of substantial completion

- July 30 , 2025

Final Completion

- Gym Addition - 06/30/2025
- Kitchen Renovation - 07/18/2025

PREPARED BY:

Kha Huynh, Carroll Daniel Construction Co.
