


Quote of the week: "What you do today can improve all of your tomorrows." — Ralph Marston

Project: Hank Aaron Academy Additions & Modifications

Week Ending: November 15, 2024

THIS WEEK:

- Completed demo at retention pond and began grading
- Began installing headwall A1 back toward underground retention pond
- Installed OCS & storm structure D1

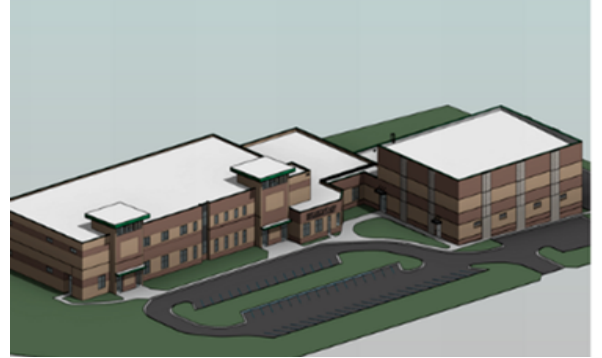

Storm Structure D1 installed



*Grading & installing filter fabric for
UDP*



Backfilling head wall A1



Installing OCS

NEXT WEEK – November 18th - November 22nd

- Continue installation of underground retention pond & associates structures
- Continue installing storm at upper parking lot
- Start fire line installation at upper parking lot

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- November 28, 2025

PREPARED BY:

Karee Shaw, Carroll Daniel Construction Co.

