


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit Center

WEEK ENDING 01/26/2024

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

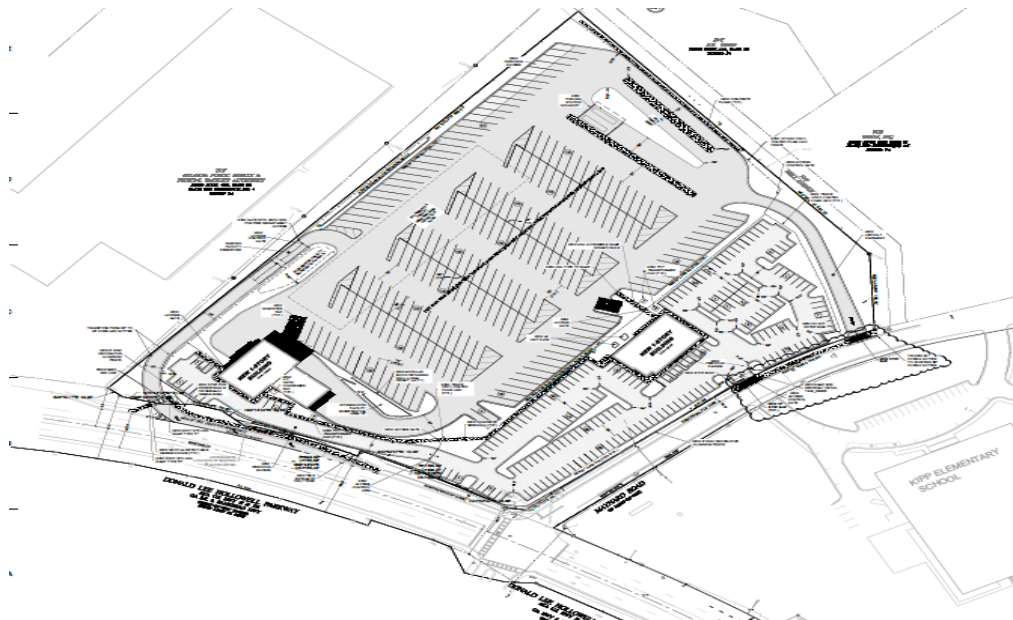

Construction Activities this week

- 85% COMPLETED WITH STORM LINES/STRUCTURES.
- 100% COMPLETED WITH OPERATIONS BUILDING PAD.
- CONCRETE PIERS/SPREAD FOOTINGS ARE INSTALLED.
- ELECTRICAL UNDERGROUND ROUGH-IN'S ARE 75% COMPLETED. TASK IS ONGOING.
- SS BORE ACROSS MAYNARD STREET WORK REMAINS ON HOLD TILL FURTHER NOTICE.
- BACKFILLING OF THE RETENTION POND 100% COMPLETED.
- FIRE RISER PIPING TO OPERATION BUILDING STUB-IN HAS BEEN RAN.
- 100% OF MASS GRADING FOR LAYDOWN AREA IS COMPLETE. EQUIPMENT AND CONEX BOXES HAVE ARRIVED ONSITE. GRAVEL TO BE LAID ON (01/29/24)
- OPERATIONS BUILDING ANCHOR BOLTS ARRIVED ONSITE (01/10/24).
- SANITARY PIPING IS ROUGHLY 25% INSTALLED UNDERGROUND.

CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

THIS IS DEPENDENT UPON PERMITTING STATUS AND WEATHER.

- CONCRETE, PLUMBING & ELECTRICAL EQUIPMENT DELIVERIES WILL CONTINUE WEEK OF (01/29/24)
- STRUCTURAL FOUNDATION LAYOUT
- UNDERSLAB PLUMBING INSTALLATION (MEP INSTALLATION) IS ONGOING.
- OPERATIONS BUILDING SLAB POURED IN PLACE IS ONGOING
- SANITARY & WATER UTILITIES SCOPE OF WORK CONTINUED.

WEEKLY CONSTRUCTION PROGRESS REPORT



MANPOWER LOG (WEEK OF 01/26/24)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	18	18	18	18	18
JAMISON CONSTRUCTION	6	6	6	6	6
PENCO ELECTRICAL	3	3	3	3	3
TEBARCO MECHANICAL	0	0	0	0	0

WEATHER LOG (MONTH OF DECEMBER/JANUARY)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (18) EIGHTEEN TRACKED RAIN DAYS IN DECEMBER/JANUARY.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23) / (12-24-23) / (12-25-23) / (12-26-23) / (01/06/24) / (01/08/24) / (01/09/24) / (01/12/24) / (01/16/24) / (01/19/24) / (01/24/24) / (01/25/24) / (01/26/24)
- TRACKED HAZARDOUS CONDITIONS DAYS: 17 DAYS

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

