


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit Center

WEEK ENDING 02/02/2024

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

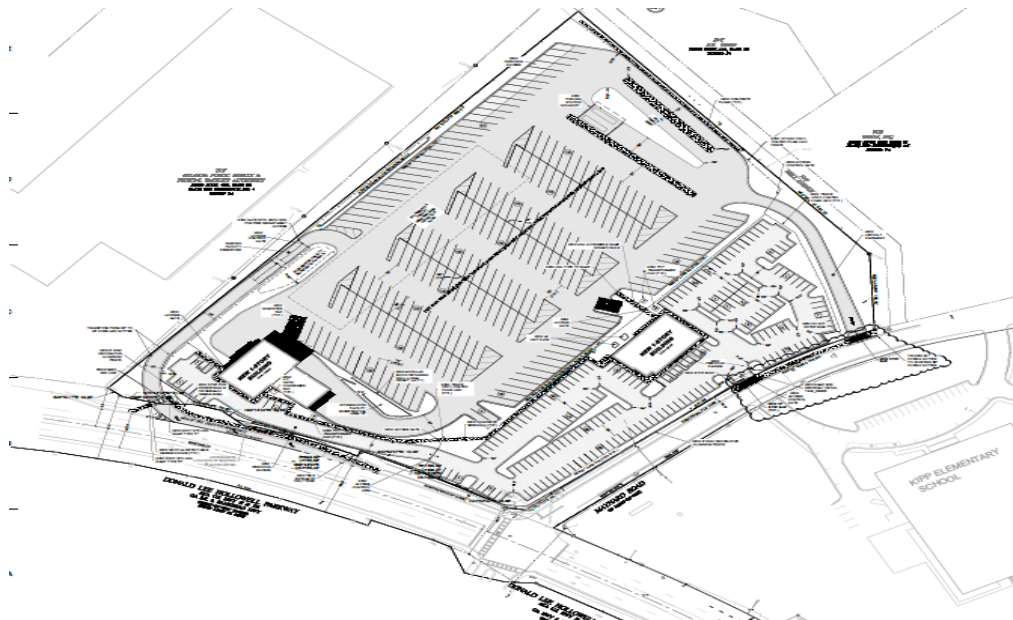

Construction Activities this week

- 85% COMPLETED WITH STORM LINES/STRUCTURES.
- CONCRETE PIERS/SPREAD FOOTINGS ARE INSTALLED AT OPERATIONS BUILDING
- ELECTRICAL/PLUMBING UNDERGROUND ROUGH-INS ARE 85% COMPLETED AT OPERATIONS BUILDING. TASK IS ONGOING.
- SS BORE ACROSS MAYNARD STREET WORK REMAINS ON HOLD TILL FURTHER NOTICE.
- FIRE RISER PIPING TO OPERATION BUILDING STUB-IN HAS BEEN RAN. INSPECTION REPORT CAME BACK POSITIVE.
- 100% OF MASS GRADING FOR LAYDOWN AREA IS COMPLETE. EQUIPMENT AND CONEX BOXES HAVE ARRIVED ONSITE. GRAVEL TO BE LAID ON (02/05/24)
- SANITARY PIPING IS ROUGHLY 35% INSTALLED UNDERGROUND.

CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

THIS IS DEPENDENT UPON PERMITTING STATUS AND WEATHER.

- CONCRETE, PLUMBING & ELECTRICAL EQUIPMENT DELIVERIES WILL CONTINUE WEEK OF (02/09/24)
- STRUCTURAL FOUNDATION LAYOUT
- UNDERSLAB PLUMBING INSTALLATION (MEP INSTALLATION) IS ONGOING.
- OPERATIONS BUILDING SLAB POURED TRACKING FOR WEEK OF (02/09/24)
- MAINTENANCE BUILDING SLAB POURED TRACKING FOR WEEK OF (02/16/24)
- SANITARY & WATER UTILITIES SCOPE OF WORK CONTINUED.

WEEKLY CONSTRUCTION PROGRESS REPORT



MANPOWER LOG (WEEK OF 02/02/24)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	15	15	15	15	15
JAMISON CONSTRUCTION	1	1	1	1	1
PENCO ELECTRICAL	2	2	2	3	2
TEBARCO MECHANICAL	5	5	5	5	5
NOVA ENGINEERING	1	1	1	1	1



WEATHER LOG (MONTH OF DECEMBER/JANUARY/FEBRUARY)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (21) TWENTY-ONE TRACKED RAIN DAYS IN DECEMBER/JANUARY/FEBRUARY.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23) / (12-24-23) / (12-25-23) / (12-26-23) / (01/06/24) / (01/08/24) / (01/09/24) / (01/12/24) / (01/16/24) / (01/19/24) / (01/24/24) / (01/25/24) / (01/26/24) / (01/27/24) / (01/28/24) / (01/29/24)
- NO TRACKED RAIN DAYS IN FEBRUARY YET.
- TRACKED INCLEMENT CONDITIONS DAYS: 26 DAYS

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

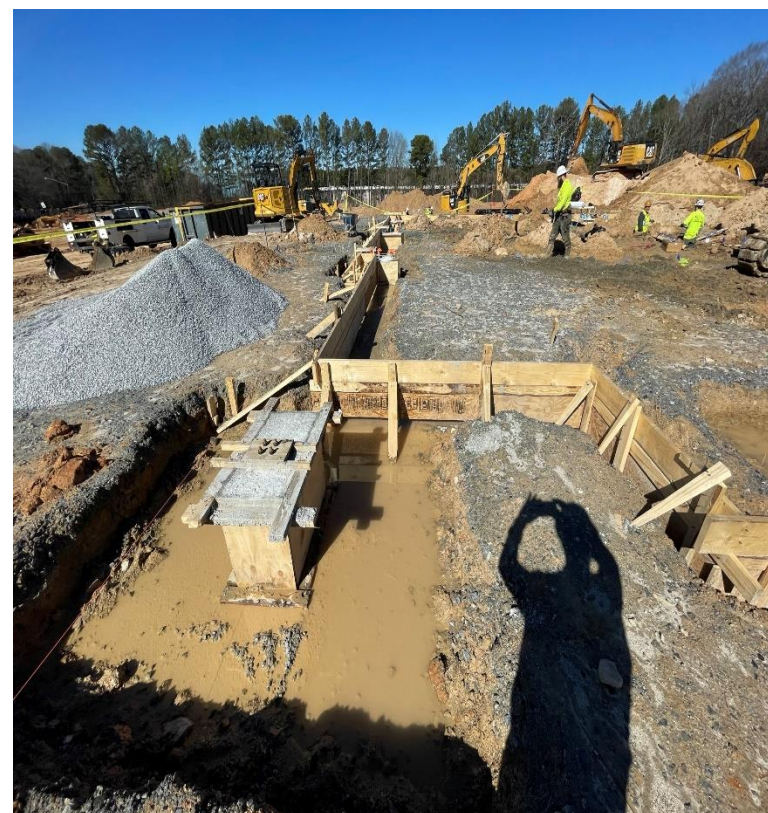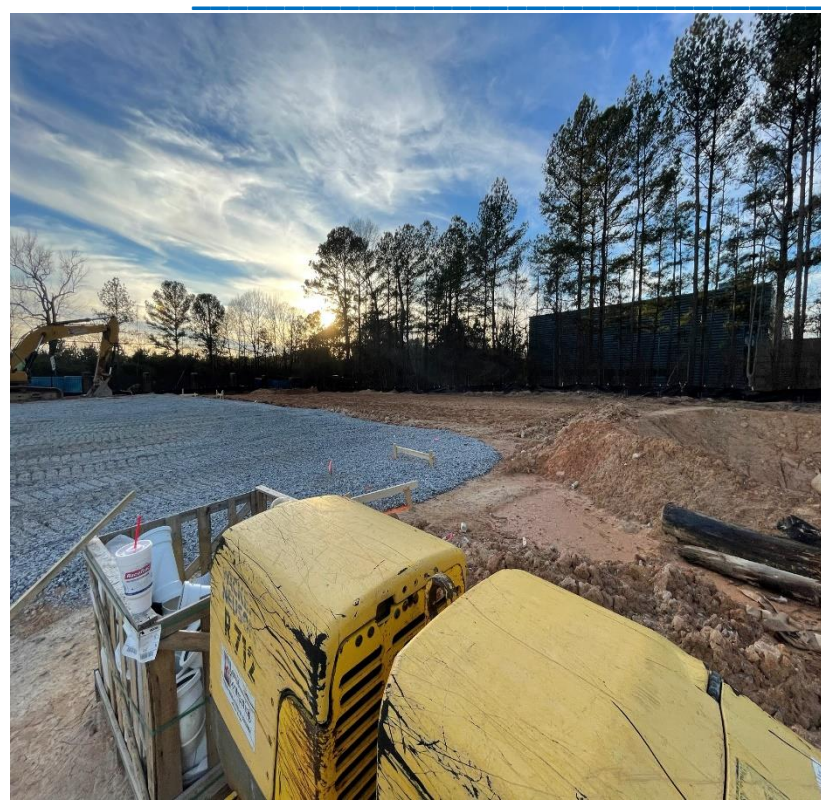

WEEKLY CONSTRUCTION PROGRESS REPORT

