


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit Center

WEEK ENDING 02/23/2024

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

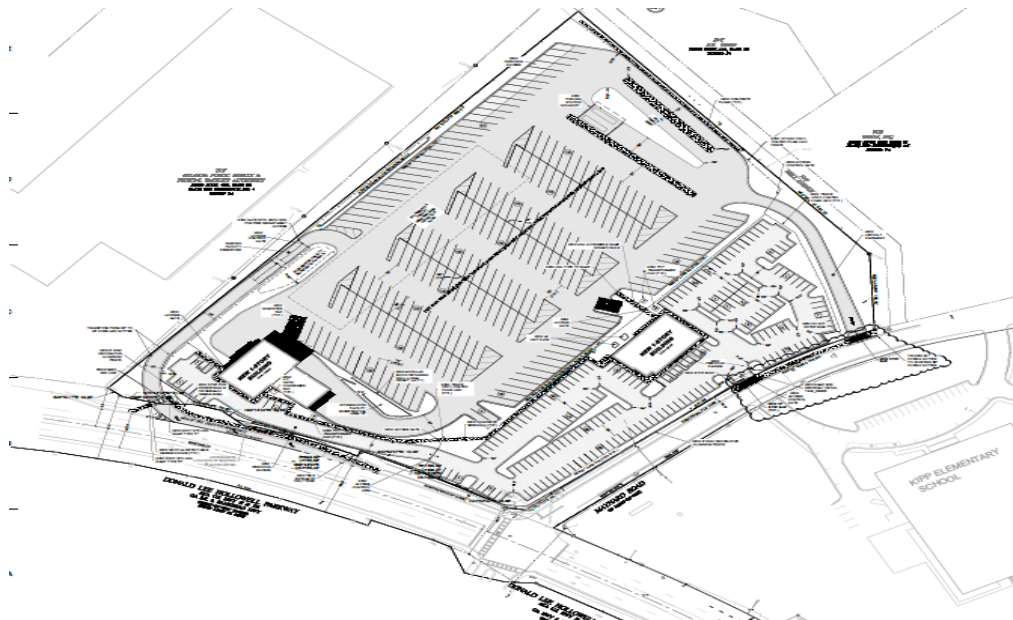

Construction Activities this week

- CONCRETE PIERS/SPREAD FOOTINGS POURS ARE ONGOING AT MAINTENANCE BUILDING.
- CMP SLOT DRAIN HAS ARRIVED AND HAS BEEN INSTALLED WEEK OF (02/23/24).
- OIL/GRIT SEPARATOR INSTALLED WEEK OF (02/23/24).
- GDOT PERMIT IS IN FINAL STAGES OF PROCESSING.
- 100% OF MASS GRADING FOR LAYDOWN AREA IS COMPLETE. EQUIPMENT AND CONEX BOXES HAVE ARRIVED ONSITE. GRAVEL HAS BEEN LAID.
- SANITARY PIPING IS ROUGHLY 55 % INSTALLED UNDERGROUND.
- MODULAR BLOCK WALL "C" INSTALLATION STARTED WEEK OF (02/23/24). WALLS "A" & "B" WILL COMMENCE SOON.
- REBAR IS IN THE PROCESS OF BEING INSTALLED AT MAINTENANCE BUILDING WEEK OF (02/23/24).
- SUBGRADE EXCAVATION HAS CONTINUOUSLY OCCURRED ONSITE. UNDERGROUND ELECTRICAL SITEWORK IS ONGOING.

CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

THIS IS DEPENDENT UPON PERMITTING STATUS AND WEATHER.

- CONCRETE, PLUMBING & ELECTRICAL EQUIPMENT DELIVERIES WILL CONTINUE WEEK OF (03/01/24)
- STRUCTURAL FOUNDATION LAYOUT
- OPERATIONS PEMB (PRE-ENGINEERED METAL BUILDING) WILL ARRIVE ONSITE WEEK OF (03/15/24). ERECTION OF THE BUILDING WILL COMMENCE THE SAME WEEK.
- CURB & GUTTER INSTALLATION WILL COMMENCE IN UPCOMING WEEKS.
- UNDERSLAB MEP INSTALLATION ARE ONGOING AT MAINTENANCE BUILDING WEEK OF (03/01/24)
- MAINTENANCE BUILDING SLAB POURED TRACKING FOR WEEK OF (03/12/24) DUE TO WEATHER AND SITE CONDITIONS.
- SANITARY & WATER UTILITIES SCOPE OF WORK CONTINUED.

WEEKLY CONSTRUCTION PROGRESS REPORT



MANPOWER LOG (WEEK OF 02/23/24)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	20	20	17	18	3
JAMISON CONSTRUCTION	2	0	2	1	0
PENCO ELECTRICAL	2	2	2	2	2
TEBARCO MECHANICAL	3	3	3	3	3
NOVA ENGINEERING	1	1	1	1	1

WEATHER LOG (MONTH OF DECEMBER/JANUARY/FEBRUARY)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (26) TWENTY-SIX TRACKED RAIN DAYS IN DECEMBER/JANUARY/FEBRUARY.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23) / (12-24-23) / (12-25-23) / (12-26-23) / (01/06/24) / (01/08/24) / (01/09/24) / (01/12/24) / (01/16/24) / (01/19/24) / (01/24/24) / (01/25/24) / (01/26/24) / (01/27/24) / (01/28/24) / (01/29/24) / (02/04/24) / (02/10/24) / (02/11/24) / (02/12/24) / (02/22/24)
- TRACKED INCLEMENT CONDITIONS DAYS: 31 DAYS

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

