


Quote of the week: "It doesn't get easier , you get better."

Project: FL Stanton ES Renovation and Addition

Week ending: April 12, 2024

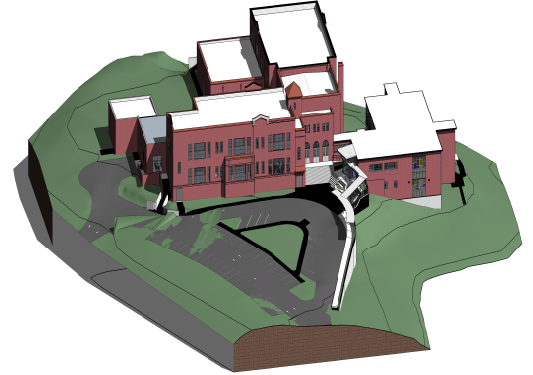

- Installing racks in the lower level MDF room
- Begin installing blocking for cafeteria windows
- Continue with VRF piping at the gym and 1958 wing
- Continue removing old feeder wires
- Continue hanging all spiral duct in the media center
- Continue electrical rough-in @ the gym
- Begin metal framing of the stage ramp in the gym



Continue Spiral duct install in the media center



Gym stage ramp metal stud framing is nearly complete



Began installing black brick at the front vestibule area



Begin installing new windows and window frames

NEXT WEEK – April 15 - April 19

- Begin grading vestibule pour back and forming sidewalks
- Continue with ceiling grid installation
- Begin resinous flooring at bathrooms
- Begin installing brackets for the stage curtains
- Continue connecting all electrical wiring and piping in HVAC units
- Continue installing storefront and replace windows
- Priming stairwell 3 , 5 and 6

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30 , 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.

